


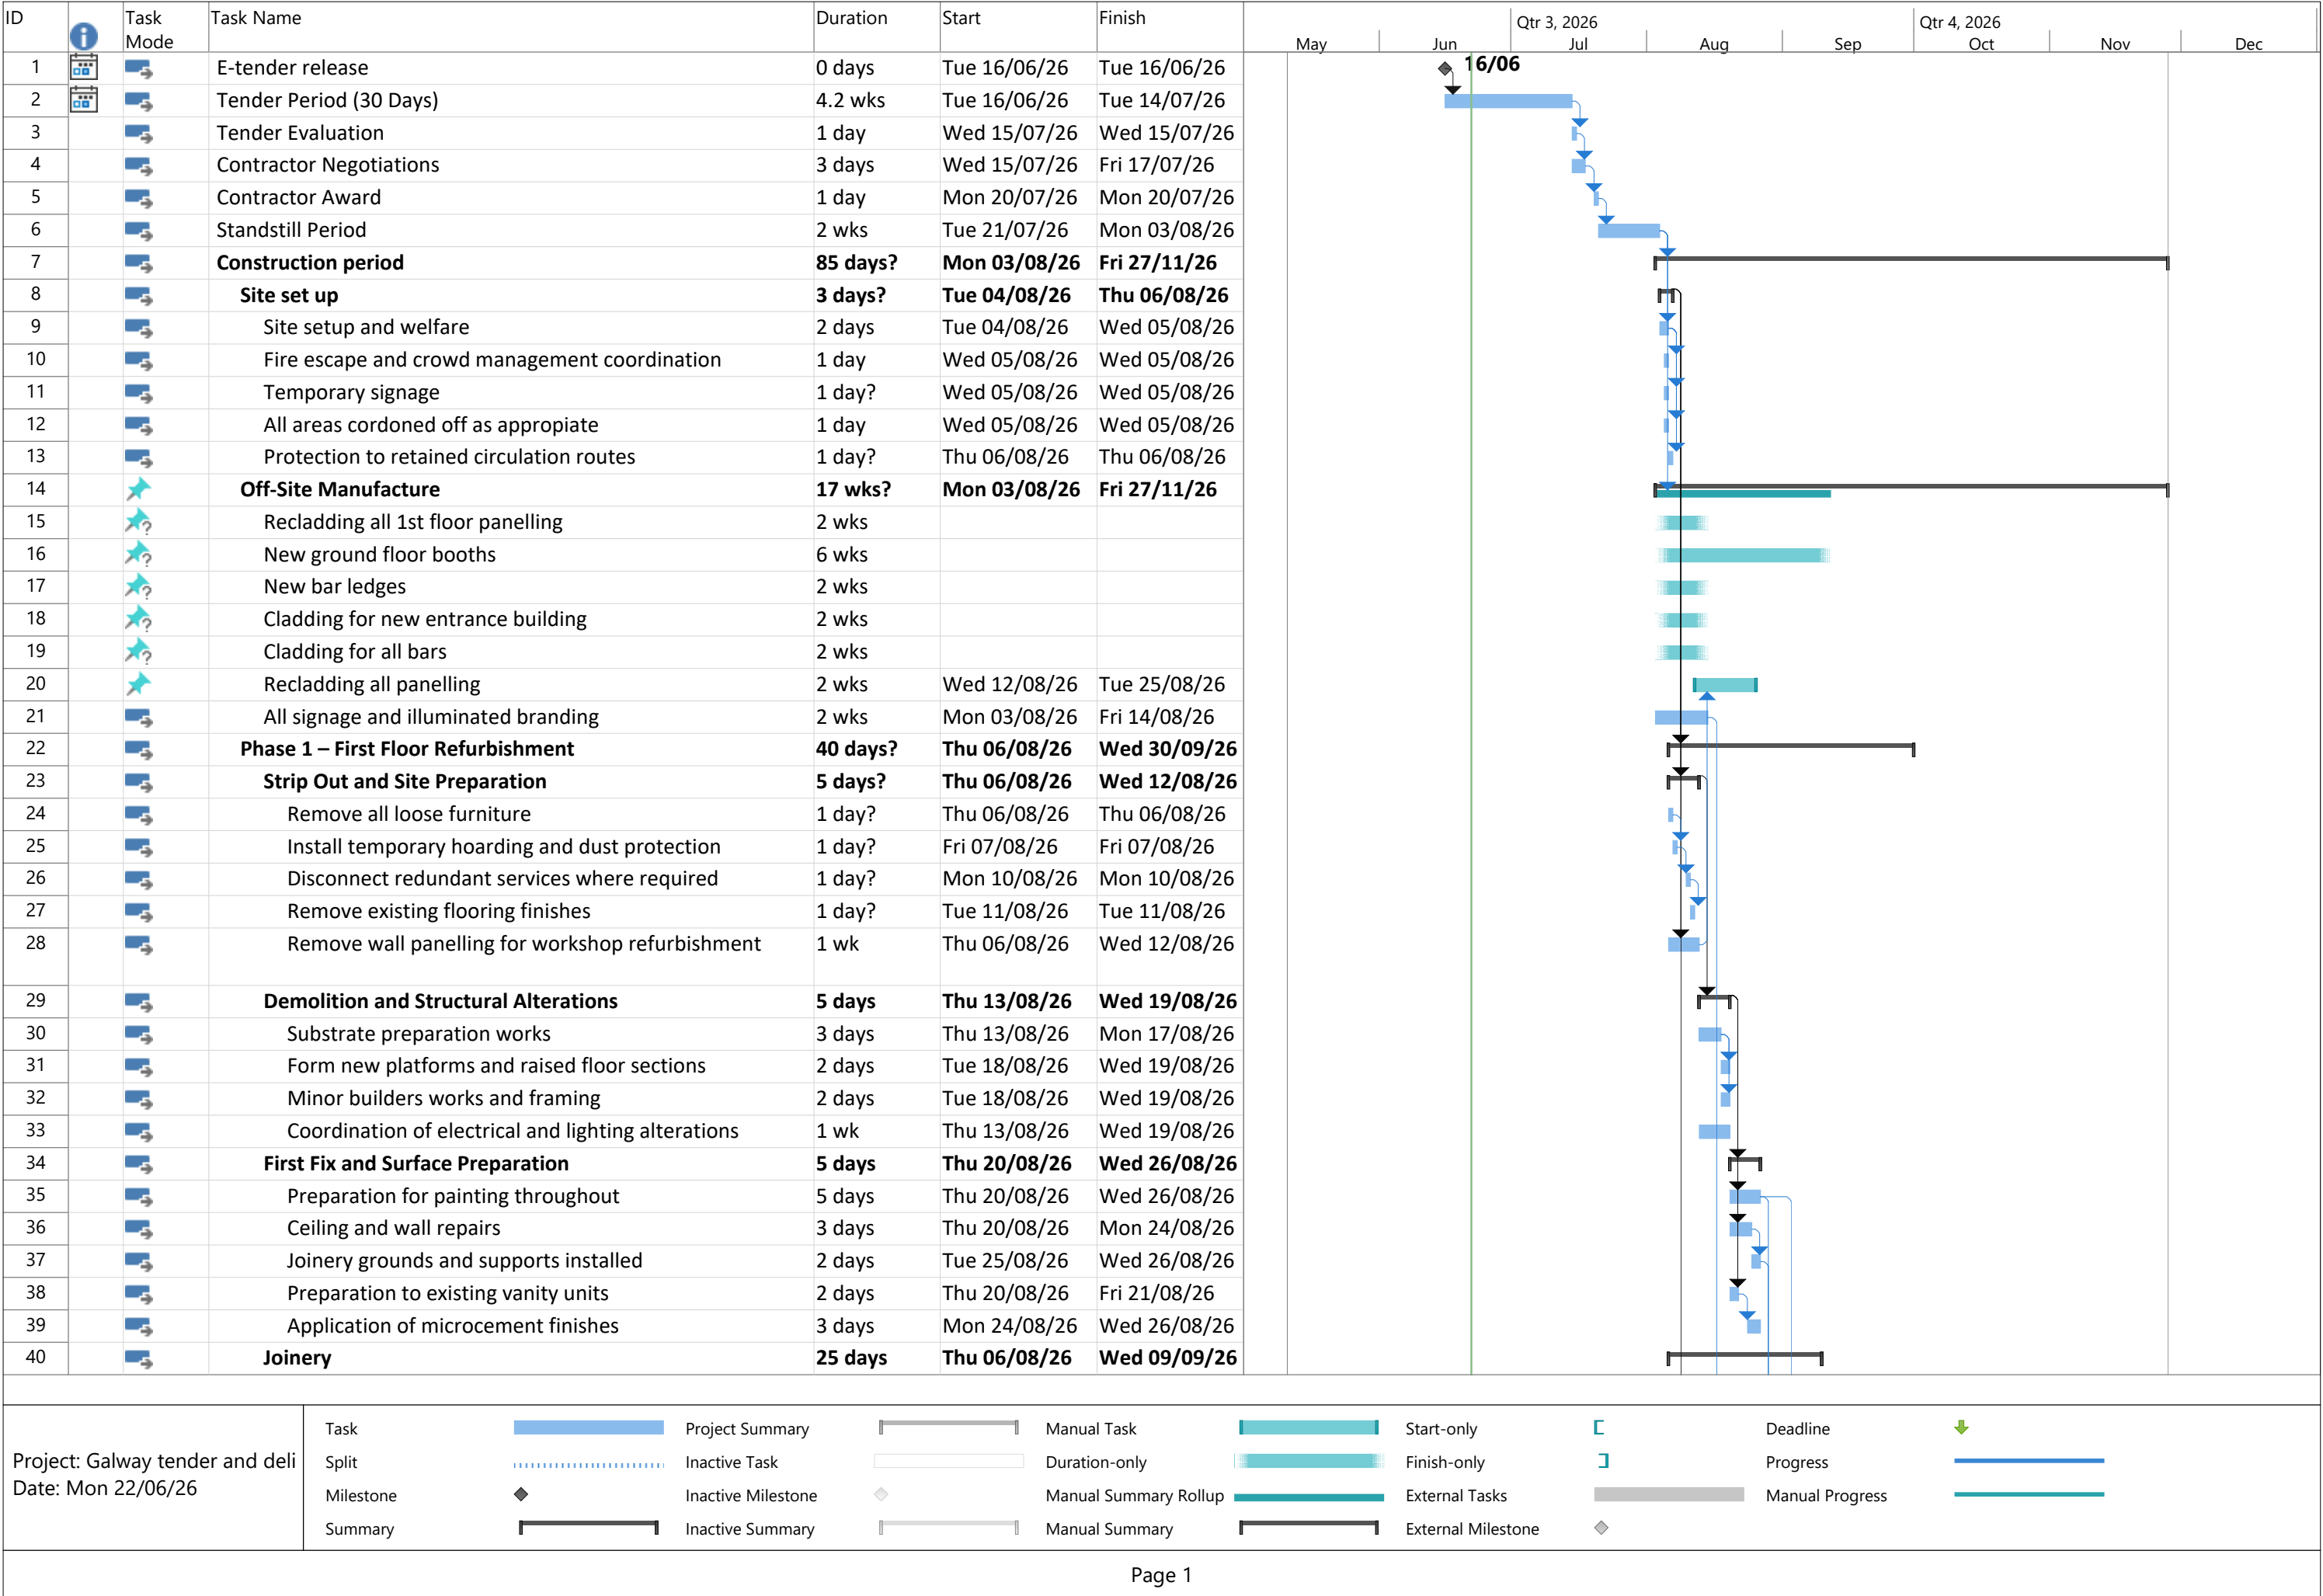

ID	i	Task Mode	Task Name	Duration	Start	Finish												
							May	Jun	Jul	Aug	Sep	Oct	Nov	Dec				
41			Reclad all bars	1 wk	Thu 06/08/26	Wed 12/08/26												
42			Install new reception desk and tote booth	2 days	Thu 06/08/26	Fri 07/08/26												
43			Reinstalled re-veneered wall panelling	2 days	Tue 08/09/26	Wed 09/09/26												
44			Flooring and Painting	15 days	Thu 27/08/26	Wed 16/09/26												
45			Paint all areas behind panelling	1 wk	Thu 27/08/26	Wed 02/09/26												
46			Painting throughout	2 wks	Thu 03/09/26	Wed 16/09/26												
47			Installation of all new floor finishes	1 wk	Thu 27/08/26	Wed 02/09/26												
48			Detailing at thresholds and interfaces	1 wk	Thu 03/09/26	Wed 09/09/26												
49			Furniture, Lighting and Commissioning	9 days?	Thu 17/09/26	Tue 29/09/26												
50			Delivery and placement of furniture	1 day?	Thu 17/09/26	Thu 17/09/26												
51			deep clean	2 days	Fri 18/09/26	Mon 21/09/26												
52			Snagging and commissioning	1 wk	Tue 22/09/26	Mon 28/09/26												
53			Final Clean	1 day?	Tue 29/09/26	Tue 29/09/26												
54			Reopening 1st floor	0 days	Wed 30/09/26	Wed 30/09/26												
55			Entrance Building Works	30 days	Fri 07/08/26	Thu 17/09/26												
56			Enabling Works	1 wk	Fri 07/08/26	Thu 13/08/26												
57			Structural Openings	1 wk	Fri 14/08/26	Thu 20/08/26												
58			Envelope and Framing Works	1 wk	Fri 21/08/26	Thu 27/08/26												
59			Glazing and Turnstile Installation	1 wk	Fri 28/08/26	Thu 03/09/26												
60			External Cladding	1 wk	Fri 04/09/26	Thu 10/09/26												
61			Signage and Completion	1 wk	Fri 11/09/26	Thu 17/09/26												
62			Phase 2 Ground Floor Refurbishment	40 days	Thu 01/10/26	Wed 25/11/26												
63			Site Preparation and Strip Out	5 days	Thu 01/10/26	Wed 07/10/26												
64			Remove carpets and redundant fittings	2 days	Thu 01/10/26	Fri 02/10/26												
65			Remove redundant cladding around structures	2 days	Mon 05/10/26	Tue 06/10/26												
66			Install hoarding and dust partitions	1 day	Wed 07/10/26	Wed 07/10/26												
67			Isolate affected areas	1 day	Wed 07/10/26	Wed 07/10/26												
68			Demolition and Builders Works	5 days	Thu 08/10/26	Wed 14/10/26												
69			Cut back existing tote booth	1 day	Thu 08/10/26	Thu 08/10/26												
70			Form new opening to hot food servery	1 day	Thu 08/10/26	Thu 08/10/26												
71			Form new cleaner store door opening	1 day	Thu 08/10/26	Thu 08/10/26												
72			Demolition of toilet block	3 days	Thu 08/10/26	Mon 12/10/26												
73			Making good to drainage and pipework	2 days	Tue 13/10/26	Wed 14/10/26												
74			Structural and Framing Works	5 days	Thu 15/10/26	Wed 21/10/26												
75			Framing and builders works	1 wk	Thu 15/10/26	Wed 21/10/26												
76			Coordination of services modifications	3 days	Thu 15/10/26	Mon 19/10/26												
77			Form new stage area	2 days	Tue 20/10/26	Wed 21/10/26												
78			Surface Preparation	10 days	Thu 15/10/26	Wed 28/10/26												
79			Preparation for painting throughout	1 wk	Thu 15/10/26	Wed 21/10/26												
80			Substrate preparation works	2 days	Thu 22/10/26	Fri 23/10/26												
81			Microcement application to existing vanities	3 days	Mon 26/10/26	Wed 28/10/26												

Project: Galway tender and deli

Date: Mon 22/06/26

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks


External Milestone

Deadline

Progress

Manual Progress

Page 2

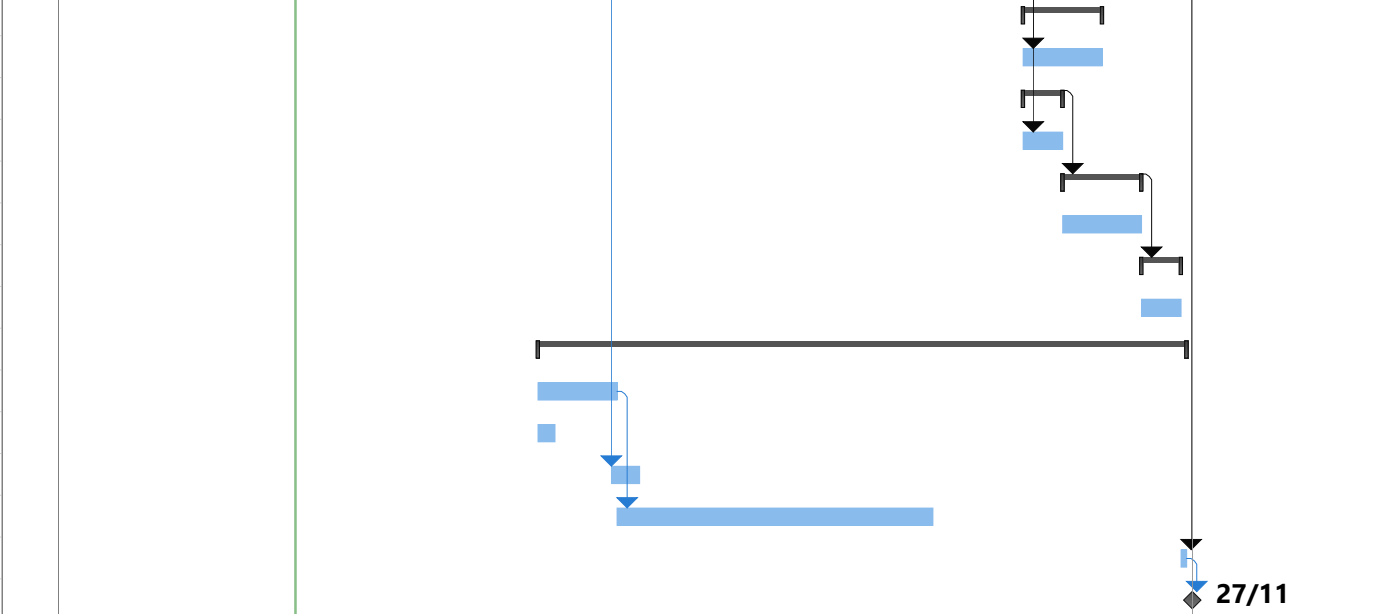ID	 Task Mode	Task Name	Duration	Start	Finish	May Jun Qtr 3, 2026 Jul Aug Sep Qtr 4, 2026 Oct Nov Dec											
82		Joinery	10 days	Thu 29/10/26	Wed 11/11/26												
83		Install all joinery items	2 wks	Thu 29/10/26	Wed 11/11/26												
84		Lighting and Ceiling Works	5 days	Thu 29/10/26	Wed 04/11/26												
85		Lighting and ceilng workd	1 wk	Thu 29/10/26	Wed 04/11/26												
86		Flooring Installation	10 days	Thu 05/11/26	Wed 18/11/26												
87		All flooring	2 wks	Thu 05/11/26	Wed 18/11/26												
88		Signage, Decoration and Completion	5 days	Thu 19/11/26	Wed 25/11/26												
89		<New Task>	1 wk	Thu 19/11/26	Wed 25/11/26												
90		External works	83 days?	Tue 04/08/26	Thu 26/11/26												
91		Form new entrance surround	2 wks	Tue 04/08/26	Mon 17/08/26												
92		Final external lighting adjustments	3 days	Tue 04/08/26	Thu 06/08/26												
93		Replace remaining external signage	1 wk	Mon 17/08/26	Fri 21/08/26												
94		Complete all external painting works	8 wks	Tue 18/08/26	Mon 12/10/26												
95		Remove temporary works and hoarding	1 day?	Thu 26/11/26	Thu 26/11/26												
96		Grand reopening	0 days	Fri 27/11/26	Fri 27/11/26												

Project: Galway tender and deli
Date: Mon 22/06/26

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Manual Task

Finish-only

External Tasks

External Milestone

Start-only

Progress

Manual Progress

Deadline

Progress

Manual Progress

Page 3
