

Think | Design | Engineer

Dernafanogy Bridge, Donegal

Project Safety and Health Plan

24200-DID-ZZ-XX-HS-C-0001

Document Details

Project:	Dernafanogy Bridge, Donegal		
Title:	Project Safety and Health Plan		
External Project Number:	N/A		
Document Reference:	24200-DID-ZZ-XX-HS-C-0001		
Design ID Project Number:	24200		
Date:	June 2026		
Current revision:	T01		
Suitability	D2		
Suitability Description	Issued for Tender		
Author	Ciara Conlon	Initial:	CC
Checked By:	Ronan Carlin	Initial:	RC

Revision	Description	Date Revised	Revised By	Checked By
P01	First Issue	08.11.2024	CC	RC
P02	Second Issue	08.10.2025	CC	RC
P03	Third Issue	11.03.2026	CC	RC
T01	Tender Issue	09.06.2026	YH	RC
T02	Tender Issue	19.06.2026	YH	RC

© Copyright Design ID

This document has been prepared for the titled project or named part thereof and should not be relied upon or used for any other project without an independent check being carried out as to its suitability and prior written authority of Design ID being obtained. Design ID accepts no responsibility or liability for the consequence of this document being used for a purpose other than the purposes for which it was commissioned. Any person using or relying on the document for such other purpose agrees, and will by such use or reliance be taken to confirm his agreement to indemnify Design ID for all loss or damage resulting there from. Design ID accepts no responsibility or liability for this document to any party other the person for whom it was commissioned.

Contents

1	Introduction.....	5
1.1.	Purpose of this Document.....	5
1.2.	Project Supervisor for the Design Process	5
1.3.	Related Legislation.....	5
1.4.	Drawings, Specification and Other Documents	6
2	Details of the Project.....	7
2.1.	Description of the Project.....	7
2.2.	Location of Works	8
2.3.	Timescales	8
2.4.	Phasing of the Works	9
2.5.	Notification of Project	9
2.6.	Project Team.....	9
2.7.	Surrounding Land Use	9
2.8.	Other Contract or Building Works Which May Affect the Project.....	10
2.9.	Contact Details for Individual Service Providers.....	10
3	Client Consideration and Management Regulations	11
3.1.	Arrangements for Planning and Managing Construction Works.....	11
3.2.	Site Specific Safety Objectives	12
3.3.	Site Rules	13
3.4.	Restrictions on Working Hours	13
3.5.	Security of the Site and Hoarding Design	13
3.6.	Welfare Provision	14
3.7.	Site Transport Arrangements or Vehicle Movement Restrictions.....	14
3.8.	Permit to Work Systems	14
3.9.	Authorisation Requirements.....	14
3.10.	Confined Spaces	14
4	Site Specific Safety Information.....	15
4.1.	Existing Services.....	15
4.2.	Emergency Procedures and Means of Escape	15
4.3.	Existing Structures	16
4.4.	Asbestos Information	16
4.5.	Ground Conditions	16
4.6.	Contaminated Land.....	16
4.7.	Liaison with Stakeholders	16
4.8.	List of Stakeholders.....	17
4.9.	Landowner Consent	17

4.10.	PSDP / PSCS Interface	17
4.11.	Design of Temporary Works.....	18
4.12.	Alterations to the Permanent Works Design	19
4.13.	Environmental Risks.....	19
5	Significant Design and Construction Hazards	20
5.1.	Particular Risks to Health, Safety and Welfare	20
5.2.	Risks to Health, Safety and Welfare	20
5.3.	Suggested Work Methods, Sequences or Control Measures	21
5.4.	Arrangements for Handling Design Changes	21
6	Safety File.....	22
6.1.	Information Required for Safety File	22
6.2.	Information Delivery Format.....	23
Appendix A – Existing Service Responses		

1 Introduction

1.1. Purpose of this Document

This Preliminary Safety and Health Plan has been prepared by the Project Supervisor Design Process (PSDP) in compliance with Regulation 12 of the Safety, Health and Welfare at Work (Construction Regulations) 2013, hereby known as 'The Regulations'.

The Preliminary Safety and Health Plan will be made available to the designated Project Supervisor Construction Stage (PSCS) in compliance with Regulation 9, who will develop it in line with Regulation 16 to include additional information unavailable prior to PSCS appointment, at which point under this Regulation it will become known as the Safety and Health Plan.

The PSDP will hold a copy of this plan to be made available for inspection by an inspector for the duration of the works.

1.2. Project Supervisor for the Design Process

Design ID Consulting Ltd (DID) have been appointed by Donegal County Council to act as The PSDP for this project. Contact details can be found in Section 2.3.

The PSDP has been appointed to oversee the coordination of designers through the project. In this role Design ID have prepared this written Preliminary Safety and Health Plan. The PSDP may issue directions to designers, contractors or other relevant parties involved in the project.

Design ID have also been appointed as Employer's Representative from Tender to Construction.

1.3. Related Legislation

This Preliminary Safety and Health Plan should be read in conjunction with the following Legislation and all subsequent Regulations and Guidelines:

- Safety, Health and Welfare at Work Act 2005
- S.I. No. 504 Safety, Health and Welfare at Work (Construction) Regulations, 2006
- S.I. No. 291 Safety, Health and Welfare at Work (Construction) Regulations, 2013
- S.I. No. 299 Safety, Health and Welfare at Work (General Application) Regulations 2007
- Guidelines and Codes of Practice as published from time to time by the HAS

1.4. Drawings, Specification and Other Documents

- Volume A: Works Requirements
- 24200-DID-ZZ-XX-DR-C-1001 Existing Site Location Plan
- 24200-DID-ZZ-XX-DR-C-1002 Plan Layouts
- 24200-DID-ZZ-XX-DR-C-1003 Sections and Details

2 Details of the Project

2.1. Description of the Project

The title of the project is Dernafanogy Bridge, hereby referred to as 'The Project'.

Design ID Consulting Ltd were commissioned by Donegal County Council, to provide Preliminary and Design Stage Services for the Project.

The bridge is located on the R254 at Doochary. The bridge has a clear span of 6.6m and carries R254 from Churchill to Doochary.

The works are anticipated to include the following:

- Site investigation
- Site set-up and clearance
- Excavation to existing concrete slab
- Installation of drainage
- Partial demolition and reconstruction of existing structures
- Deconstruction of temporary structures
- Construction of retaining walls and ancillary concrete
- Backfill
- Cladding parapet walls
- Reinforced concrete works
- Site clearance and mobilisation

Refer to Volume A: Works Requirements for detail design plans showing the extent and types of work to be carried out.

2.2. Location of Works

The site is located adjacent to the village of Doochary, within the townland of Derrynacarrow, County Donegal. The bridge carries the road from Churchill to Doochary across the Sruhancrocam River. Refer to 24200-DID-ZZ-XX-DR-C-1001 Existing Site Location Plan for further details.



Figure 1: Site Location

2.3. Timescales

Timescale for Construction Work		
Key Event	Date	Duration (Weeks)
Minimum mobilisation period for preparation and planning	N/A	TBC
Anticipated start date for the Construction Phase	N/A	16
Anticipated Completion Date	N/A	N/A

The PSCS shall devise a comprehensive works programme in accordance with the requirements of the Works Requirement Specification.

The PSCS must consider the timeframe stated and inform the PSDP if they feel this timeframe is not adequate for the safe completion of the works for full compliance under The Regulations. If the PSCS does not consider the proposed contract period adequate, they should set out the contract period that they feel is necessary to safely complete the works, together with their basis for calculating such a contract period, in the Programme aspect of the Instruction to Tenderers and Technical Merit Submission. Under such circumstances, their tender should be based on this longer contract period.

2.4. Phasing of the Works

The PSCS is responsible for producing a programme that illustrates adequate phasing to complete the works in accordance with the Project Design, Specification, Screening Report for Appropriate Assessment and relevant Legislation.

2.5. Notification of Project

The PSCS shall, before the work begins, give written notice promptly to the Authority in a form and containing the particulars listed in Schedule 3, sent either:

- (a) by registered post, or
- (b) as may be directed from time to time by the Authority.

It shall be the duty of the PSCS to clearly display, and periodically update the particulars required to be in any notice under Regulation 22 of the Regulations.

2.6. Project Team

Project Team Contact Details		
Duty Holder	Name	Contact Details
Employer	Donegal County Council Mark McGloin	County House Lifford County Donegal +353 74 91 53900 info@donegalcoco.ie
Project Supervisor Design Process	Design ID Ronan Carlin	23 Lisburn Road Hillsborough County Down Northern Ireland +442892681055
Employer's Representative	Design ID Mark Ronney	23 Lisburn Road Hillsborough County Down Northern Ireland +442892681055
Project Supervisor Construction Stage	TBC	TBC

2.7. Surrounding Land Use

The bridge carries the R254 over the Sruhancrocam River.

Refer to 24200-DID-ZZ-XX-DR-C-1001 Site General Arrangement for further information.

2.8. Other Contract or Building Works Which May Affect the Project

The PSCS will be the sole occupier of the site for the duration of the contract. The PSCS should ensure the safety of members of the public at all times in relation to interfaces of their works. This includes, but is not limited to, if the PSCS is working in an area, leaving an incomplete area overnight, or for an extended period without supervision then they must ensure that public access is prevented and that the works area, excavations, plant, materials are left in a safe and secure manner.

The PSCS should be aware that there may be ongoing construction works adjacent to the Site as undertaken by Council Operatives. The PSCS for this project will be expected to cooperate and coordinate with any adjacent projects for the safety of all works.

2.9. Contact Details for Individual Service Providers

Service Provider Contact Details	
Service Provider	Contact Details
ESB Networks	St. Margaret's Road, Finglas, Dublin 11
Gas Networks Ireland	Networks Services Centre St. Margaret's Road Finglas Dublin 11 D11 Y895TBC
Irish Water	24-26 Talbot Street Dublin 1 D01 NP86TBC
Aurora Telecom	St Margaret's Rd, Finglas, Dublin 11 D11 RD37
Eir Networks	Click Before You Dig: https://cbyd.emaps.eircom.ie/Eircom-CBYD/

3 Client Consideration and Management Regulations

3.1. Arrangements for Planning and Managing Construction Works

The works are instructed by the Client, are detailed in Section 1.1.

An outline of the arrangements for planning and managing health and safety during the construction phase of the project is listed below:

- i. The PSCS is responsible for the health, safety and wellbeing of all their employees at work, the health, safety and wellbeing within the construction site and of those not in their employment, who are affected by the works.
- ii. The PSCS shall be responsible for the management and implementation of health and safety on site.
- iii. The Client shall have the right to suspend the construction work if they believe that a person's safety is at risk.
- iv. The Client requires that all work is undertaken in accordance with all statutory requirements with respect to health and safety. In addition, all relevant approved codes of practice and guidance notes shall be adhered to.
- v. All personnel on site must have received adequate training to undertake their work in a safe and competent manner. Information on the training of personnel, refresher training and statutory training certification should be held by the PSCS and must be available for inspection at the site.
- vi. All persons on site should be given a site-specific induction to familiarise themselves with emergency procedures, management requirements and specific site details.
- vii. Any training needs identified as being required during the course of the project shall be undertaken. These may be in the form of toolbox talks or other suitable methods.
- viii. Health and safety shall be included on the agenda of all site meetings and significant items recorded and distributed to all relevant parties.
- ix. A system of monitoring the construction works to ensure the effective management of safety throughout the project duration shall be implemented by the PSCS. Such monitoring shall include workplace inspections for general site safety, statutory inspections including but not limited to scaffold, plant, equipment, and the monitoring of subcontractors.
- x. The PSCS is responsible for the production of all required method statements and risk assessments with respect to their undertakings. In addition, the PSCS shall review the method

statements and risk assessments of all subcontractors on site and ensure that their content is suitable and sufficient before permitting any relevant activities to commence.

- xi. Details of all accidents on site and the findings of accident investigations shall be forwarded promptly to the Employer's Representative.

3.2. Site Specific Safety Objectives

The works shall be carried out in a safe manner and with regard to the principles of prevention.

The PSCS should comply with all relevant Legislation, guidance and best practice. They should ensure the highest possible standards to provide of a workplace that is free from risks to the health, safety and welfare of persons at work or affected by their work, so far as is reasonably practicable.

The following safety objectives shall be adopted for this project:

- To have no enforcement action taken over the duration of the project.
- To eliminate all accidents and potential sources of ill health that could occur within the project.
- To have no occupational ill health arising from the project.
- To ensure that no environmental damage occurs.
- To establish safe working practices for all employees and subcontractors working on this contract.
- To develop a high degree of awareness in health, safety and environmental issues.
- To provide information and training on health and safety and to encourage employees and subcontractors to participate in meeting the requirements of the legislation to enable the contract to be completed safely.
- To ensure the least disruption to local businesses and members of the public as a result of the project.
- To exclude unauthorised persons from the work site.
- To provide safe access to and egress from the site.
- To ensure no injury or harm to any members of the public.
- To provide operating conditions so that the lowest reasonably practicable noise levels are maintained.
- To ensure that dust and odour nuisance does not occur, so far, as is reasonably practicable.
- To provide a high standard of welfare facilities for persons at work in accordance with current Legislation.

3.3. Site Rules

The PSCS shall establish site safety rules in accordance with best practice and current Construction regulations. The site safety rules should cover, but not be limited to, topics such as:

- Personal protective equipment
- Use of radios and mobile phones
- Smoking
- Restricted areas
- Hot works
- Traffic management systems
- Pedestrian routes
- Site tidiness
- Fire prevention
- Permit-to-work systems
- Emergency arrangements
- Safe use of tools and plant
- Infectious disease precautions
- Leptospirosis

The rules should be clear and easily understandable and should be brought to the attention of everyone on site who should be expected to follow them. Any special requirements such as the need to have translations of the rules available for non-English speaking workers on site should be considered.

Every site worker should be given a suitable site induction. The induction should be site specific and highlight any particular risks.

3.4. Restrictions on Working Hours

The working hours within the Site shall be as stated in Appendix 1/9 of the Works Requirement Specification.

3.5. Security of the Site and Hoarding Design

The PSCS is entirely responsible for the security of the site and should ensure unauthorised persons cannot enter into work areas while construction activities are taking place.

The PSCS is to ensure that there is an adequate temporary fencing to prevent access to the site of all un-authorized persons.

3.6. Welfare Provision

The PSCS is required to provide their own facilities that comply with the requirements of Part 14 of the Regulations. These are to be established before any construction activity commences on site and maintained in a hygienic manner for the duration of the project.

3.7. Site Transport Arrangements or Vehicle Movement Restrictions

It is the responsibility of the PSCS to determine suitability of site transport and vehicle movement restrictions in addition to access and egress.

3.8. Permit to Work Systems

The PSCS shall, implement a permit to work system for higher risk works activities.

3.9. Authorisation Requirements

The PSCS shall work within the 'Contractor's Site Area' as defined by Donegal County Council.

3.10. Confined Spaces

All works involving work on or entry into confined spaces shall be carried out in accordance with the requirements of the Regulations and shall be subject to a safe system of work and the issue of a confined spaces permit to work, as appropriate.

4 Site Specific Safety Information

4.1. Existing Services

The PSDP liaised with the major utility providers and asked them to provide records of their existing networks in the vicinity of the proposed works. Responses have been received and included in Appendix A. Overhead telecom lines are present in the surrounding area. It is the PSCS's responsibility to carry out their own existing services search, and to take all reasonable precautions when working on site with regard to undiscovered services.

In the event that an existing service is located, the PSCS shall inform the PSDP and liaise with the respective utility provider.

The PSCS shall liaise with all relevant bodies to determine the location of all services and comply with:

- 1 Code of Practice for Avoiding Danger from Underground Services (HSA 2010)
- 2 Code of Practice for Avoiding Danger from Overhead Electricity Lines (HSA/ESB 2008)

4.2. Emergency Procedures and Means of Escape

It is the responsibility of the PSCS to set in place emergency procedures for any reasonably predictable event. Emergency procedures should be well communicated and made available to all personnel involved with the Project. The procedures should make particular reference to the rescue of personnel from water where appropriate. Potential emergency contact details are included below for information only.

The PSCS shall ensure that emergency procedures and means of escape are maintained throughout the Construction Phase and any additional measures as a result of the works or erection of scaffolding/hoarding, etc. on site are put in place and maintained as required.

Local Emergency Services (Nearest) It is the PSCS's responsibility to confirm and update the below, it has been included for information only.		
Stakeholder	Name	Contact Details
Accident and Emergency Department	Letterkenny University Hospital	Kilmacrennan Rd, Letterkenny, Donegal, F92 AE81 +353 74 912 5888
Police Station	An Clochán Liath Garda Station	Main Street, Dungloe, Donegal, F94 FH94, +353 74 952 1000
Fire Station	Glenties Fire Station	Mill Rd, Glenties, Donegal In event of emergency dial 999

4.3. Existing Structures

Drawing 24200-DID-ZZ-XX-DR-C-1001 Site General Arrangement details existing structures on the Site.

4.4. Asbestos Information

There is no known asbestos on the Site.

The PSCS must ascertain if any additional information is required to ensure the safety of all persons and the works.

4.5. Ground Conditions

The general site geology comprises of peat and organic and mineral soil, according to General Soils Map (Ireland) prepared and published the National Soils Survey.

Ground outcrops of exposed rock at the surface of the ground observed during site visit.

4.6. Contaminated Land

Ecological surveys did not identify any contamination or pollution risks in the surrounding habitats. The works are confined to existing road infrastructure.

4.7. Liaison with Stakeholders

Requirements for Liaison with Stakeholders	
Local Authority	Liaise in relation to road closures, road openings, utilities, access point from the public road to the site and closing of any footpath areas adjacent to the site.
Emergency Services	Liaise in relation to emergency procedures, hazards on site, access to the site, any other relevant procedures or information.
National Monuments Service	Liaise in relation to existing known archaeology and proposed works.
Utility Providers	Liaise in relation to service and infrastructure location requests, disconnections, emergency strikes.
Inland Fisheries Ireland / National Parks and Wildlife Service	Liaise in relation to works that may impact the waterway or habitats
Landowners	Adjacent landowners have been made aware of the project.

4.8. List of Stakeholders

Stakeholders Contact Details		
Stakeholder	Name	Address Contact Details (telephone, email)
All stakeholder contact details to be confirmed with Donegal County Council by PSCS prior to construction works. This is to include local landowners, members of the public and those who use the watercourse for recreational purposes (anglers).		

4.9. Landowner Consent

The site is adjacent to private lands, in addition to the Sruhancrocam River.

Donegal County Council shall communicate with all landowners in advance of the proposed works and inform them of the details of the contract, requesting their co-operation in relation to site access. Donegal County Council will be responsible for dealing with landowner consent and will provide the PSCS with appropriate details regarding landowners where required. The PSCS shall liaise with any landowners in advance of the works to arrange site access.

Where landowner consent is not granted, the PSCS shall not enter on to the property and shall revert to the PSDP to seek instruction on how to proceed.

It is not anticipated that additional land will be required permanently or temporarily in the construction phase to deliver the final solution. The PSCS shall review the design documents and confirm this as part of their Tender.

It is the responsibility for the PSCS to carry out liaisons with Waterways Ireland in advance of the works where relevant.

4.10. PSDP / PSCS Interface

Health and safety will form a key part of the agenda at the site start-up meeting, where the PSDP will fully brief the PSCS on any safety and health concerns, pass on all relevant health and safety documentation and to inform them of their health and safety responsibilities during the construction period. At this meeting the PSCS will be required to issue a comprehensive list of all temporary and permanent work designs envisaged for the project and a schedule of anticipated delivery dates.

The PSDP may, depending on the issued information from the PSCS design team, revise and re-issue the preliminary safety and health plan for the project.

4.11. Design of Temporary Works

The PSCS should design, supply and install all temporary works in accordance with Appendix 1/11 and 1/71 of the Works Requirement Specification.

All temporary works necessary to facilitate the permanent works must be designed and assessed by competent personnel and a Temporary Works Design Certificate completed. The PSCS will be required to communicate to the PSDP all temporary works before they are implemented. This should be done in writing. Temporary works should not be installed until the temporary works design certificate has been accepted by the PSDP.

The PSCS / Temporary Works Designer must submit suitable information to support temporary works design certificates to the PSDP. Examples of information required include:

- Site investigation information
- Temporary works system envisaged
- Any potential impact on permanent works design
- Appropriate banners and warning signs shall be provided and displayed in accordance with the Construction Regulations.

Temporary works include but are not limited to:

- Fencing off / hoarding of the site for the project including appropriate supports to the fencing.
- Traffic management
- Temporary Retention structures adjacent to and/ or in waterways
- Working platforms for lifting operations
- Concrete formwork
- Excavation support/protection
- Scaffolding

The PSCS is to provide PSDP with any standard designs to be used for temporary works for review. If temporary works are installed in accordance with a pre-approved existing design the work can proceed without PSDP's sign off. However, it is required that the PSCS provides details of all temporary works (including pre-designed) completed at the next PSDP/PSCS interface, along with confirmation that it was done in accordance with the preapproved design.

4.12. Alterations to the Permanent Works Design

Any changes to the permanent works design required at the construction stage must be subject to the Design Change Process and co-ordinated by the PSDP. To this end any amendments to the original design must be brought to the PSDP's attention by the PSCS and not carried out on site until the PSDP has given approval for the amendment.

The responsibility for bringing additional design on the project (e.g. re-design and temporary works design) during the construction stage to the attention of the PSDP rests with PSCS. The PSDP will then organise co-operation between the relevant parties regarding the health and safety aspects of the design work.

In addition to design work (as above) The PSCS shall bring all unforeseen events that occur during project execution and that require changes to the design or which might affect the Particular Risks, contract period, or have other health and safety implications, to the attention of the PSDP.

4.13. Environmental Risks

Ecological surveys have been completed by Flynn Furney Environmental Consultants in July 2025. These included assessments of habitats, aquatic species, mammals, birds, and invasive species.

No Annex I habitats were found within the immediate works area. No evidence of Otter or Freshwater Pearl Mussel was found at the site. The Owenwee River downstream may support suitable habitat, but no instream works are proposed. No invasive species listed under Schedule 3 of the Wildlife Acts were found on or near the site.

This survey thus ensured that the works were compliant with:

- Planning and Development Acts, 2000–2017
- The Water Framework Directive
- The Waste Management Acts, 1996–2011
- The Environmental Protection Agency Acts, 1992–2011
- Wildlife Act, 1976, as amended by the Wildlife (Amendment) Act, 2000
- European Communities (Natural Habitats) Regulations (S.I. 94 of 1997), as amended.

For further information please refer to Volume A – Part 1 – Specification and Screening Report for Appropriate Assessment.

5 Significant Design and Construction Hazards

5.1. Particular Risks to Health, Safety and Welfare

Schedule 1: Non-exhaustive List of Work Involving Particular Risks to the Safety, Health and Welfare of Persons at Work		Risk Present?
1. Work which puts persons at work at risk of:		
(a)	Falling from a height,	✓
(b)	Burial under earthfalls,	✓
(c)	Engulfment in swampland	
where the risk is particularly aggravated by the nature of the work or processes used or by the environment at the place of work or construction site		
2.	Work which puts persons at work at risk from chemical or biological substances constituting a particular danger to the safety and health of such persons or involving a statutory requirement for health monitoring.	
3.	Work with ionising radiation requiring the designation of controlled or supervised areas as defined in Directive 96/29/Euratom ⁴ .	
4.	Work near high voltage power lines.	TBC
5.	Work exposing persons at work to the risk of drowning.	✓
6.	Work on wells, underground earthworks and tunnels.	✓
7.	Work carried out by divers at work having a system of air supply.	
8.	Work carried out in a caisson with a compressed-air atmosphere.	
9.	Work involving the use of explosives.	
10.	Work involving the assembly or dismantling of heavy prefabricated components.	✓

5.2. Risks to Health, Safety and Welfare

The following health and safety risks should be considered by the PSCS when proposing methodologies for this project and when carrying out the works. This is not an exhaustive list and is included for information only: the PSCS is responsible for the health and safety of all stakeholders for the duration of the works and should apply the general principles of prevention in a consistent manner in accordance with Schedule 2 of The Regulations in order to protect the safety, health and welfare of those at work.

Significant risks:

- Work on and around partially collapsed structures with unknown stability and unknown nature of existing foundations in addition to masonry and mortar loss to existing structures leading to potential instability

- Restriction of movement of plant due to presence of trees and vegetation
- Narrow road and the constrained nature of some elements will lead to site vehicles working in close proximity to workers
- The location of the works will lead to interfaces with members of the public and public highways

Ecological risks have been assessed and are considered minimal due to the nature and location of the works. No instream works are proposed, and the use of precast elements reduces pollution risk.

Further risks and proposed control measures are given in the PSDP Risk Assessment (24200-DID-ZZ-XX-RA-C-0001). For additional risks relating to the existing site please refer to Design ID Drawing 24200-DID-ZZ-XX-DR-C-1002 Existing Site Constraints.

5.3. Suggested Work Methods, Sequences or Control Measures

All work methods, sequences, and control measures will adhere to industry-accepted best practices, relevant regulatory standards, and applicable codes of practice. These guidelines should ensure that all tasks are performed in a safe and compliant manner, prioritising the health and safety of all personnel and stakeholders involved in the project. Any updates or modifications to the work methods or control measures will be evaluated and implemented in line with current industry standards and safety regulations.

5.4. Arrangements for Handling Design Changes

If, due to unforeseen circumstance there are aspects of design which require modification post tender and these significantly affect health and safety the following procedure shall apply.

Arrangements for handling design changes are as per the Standard Conditions of Contract.

6 Safety File

6.1. Information Required for Safety File

In accordance with Regulation 21 of The Regulations 2013, the PSCS shall:

(a) coordinate arrangements among Contractors to ensure the provision of relevant information, in writing, necessary for the PSDP to complete the safety file referred to in Regulation 13, monitor the implementation of the arrangements and take any necessary corrective action, as set out in Regulation 20, and

(b) provide in writing to the PSDP all relevant information necessary for that project supervisor to complete the safety file referred to in Regulation 13.

The PSCS is to provide all information in hard copy.

The following documentation will be required from The PSCS for inclusion in the Safety File:


- General Project Information
 - Project Supervisor Construction Stage (PSCS) contact details
 - Sub-Project Supervisor Construction Stage (PSCS) contact details
 - Project Supervisor Construction Stage (PSCS) designer details
- Design Information
 - Project Supervisor Construction Stage (PSCS) designed elements, e.g. plant / equipment / landscaping / etc.
- Construction Materials
 - Specification or data sheets for all materials installed as part of The Works.
 - Materials not in accordance with original specification
 - Hazardous Materials – Material Safety Data Sheets / COSHH sheets
- As Built Drawings and Record Information
 - As Built Drawings including mark up of design drawings.
 - Inspection and testing records
 - All information required in accordance with Quality Management System
- Operational Restrictions and Maintenance Procedures
 - Operating and Maintenance Manuals
 - Maintenance Procedures
 - Recommendations for decommissioning

- Key Operational / Health & Safety Information
 - Building services and utilities including any changes to the services on site and any amended drainage, site lighting and layouts or similar function.
 - Emergency procedures
 - Emergency and fire safety information
 - Firefighting equipment
 - Emergency lighting
 - Electrical, gas and water cut off points
- Surveys and Relevant Reports
 - Site survey information
 - Ground or site investigation survey information arising from PSCS works

6.2. Information Delivery Format

The file shall be provided in a single indexed electronic document format (including all manufacturers' data, drawings, etc). In addition, separate electronic copies of drawings in AutoCAD, and editable word or excel documents shall be provided.

Appendix A – Existing Service Responses

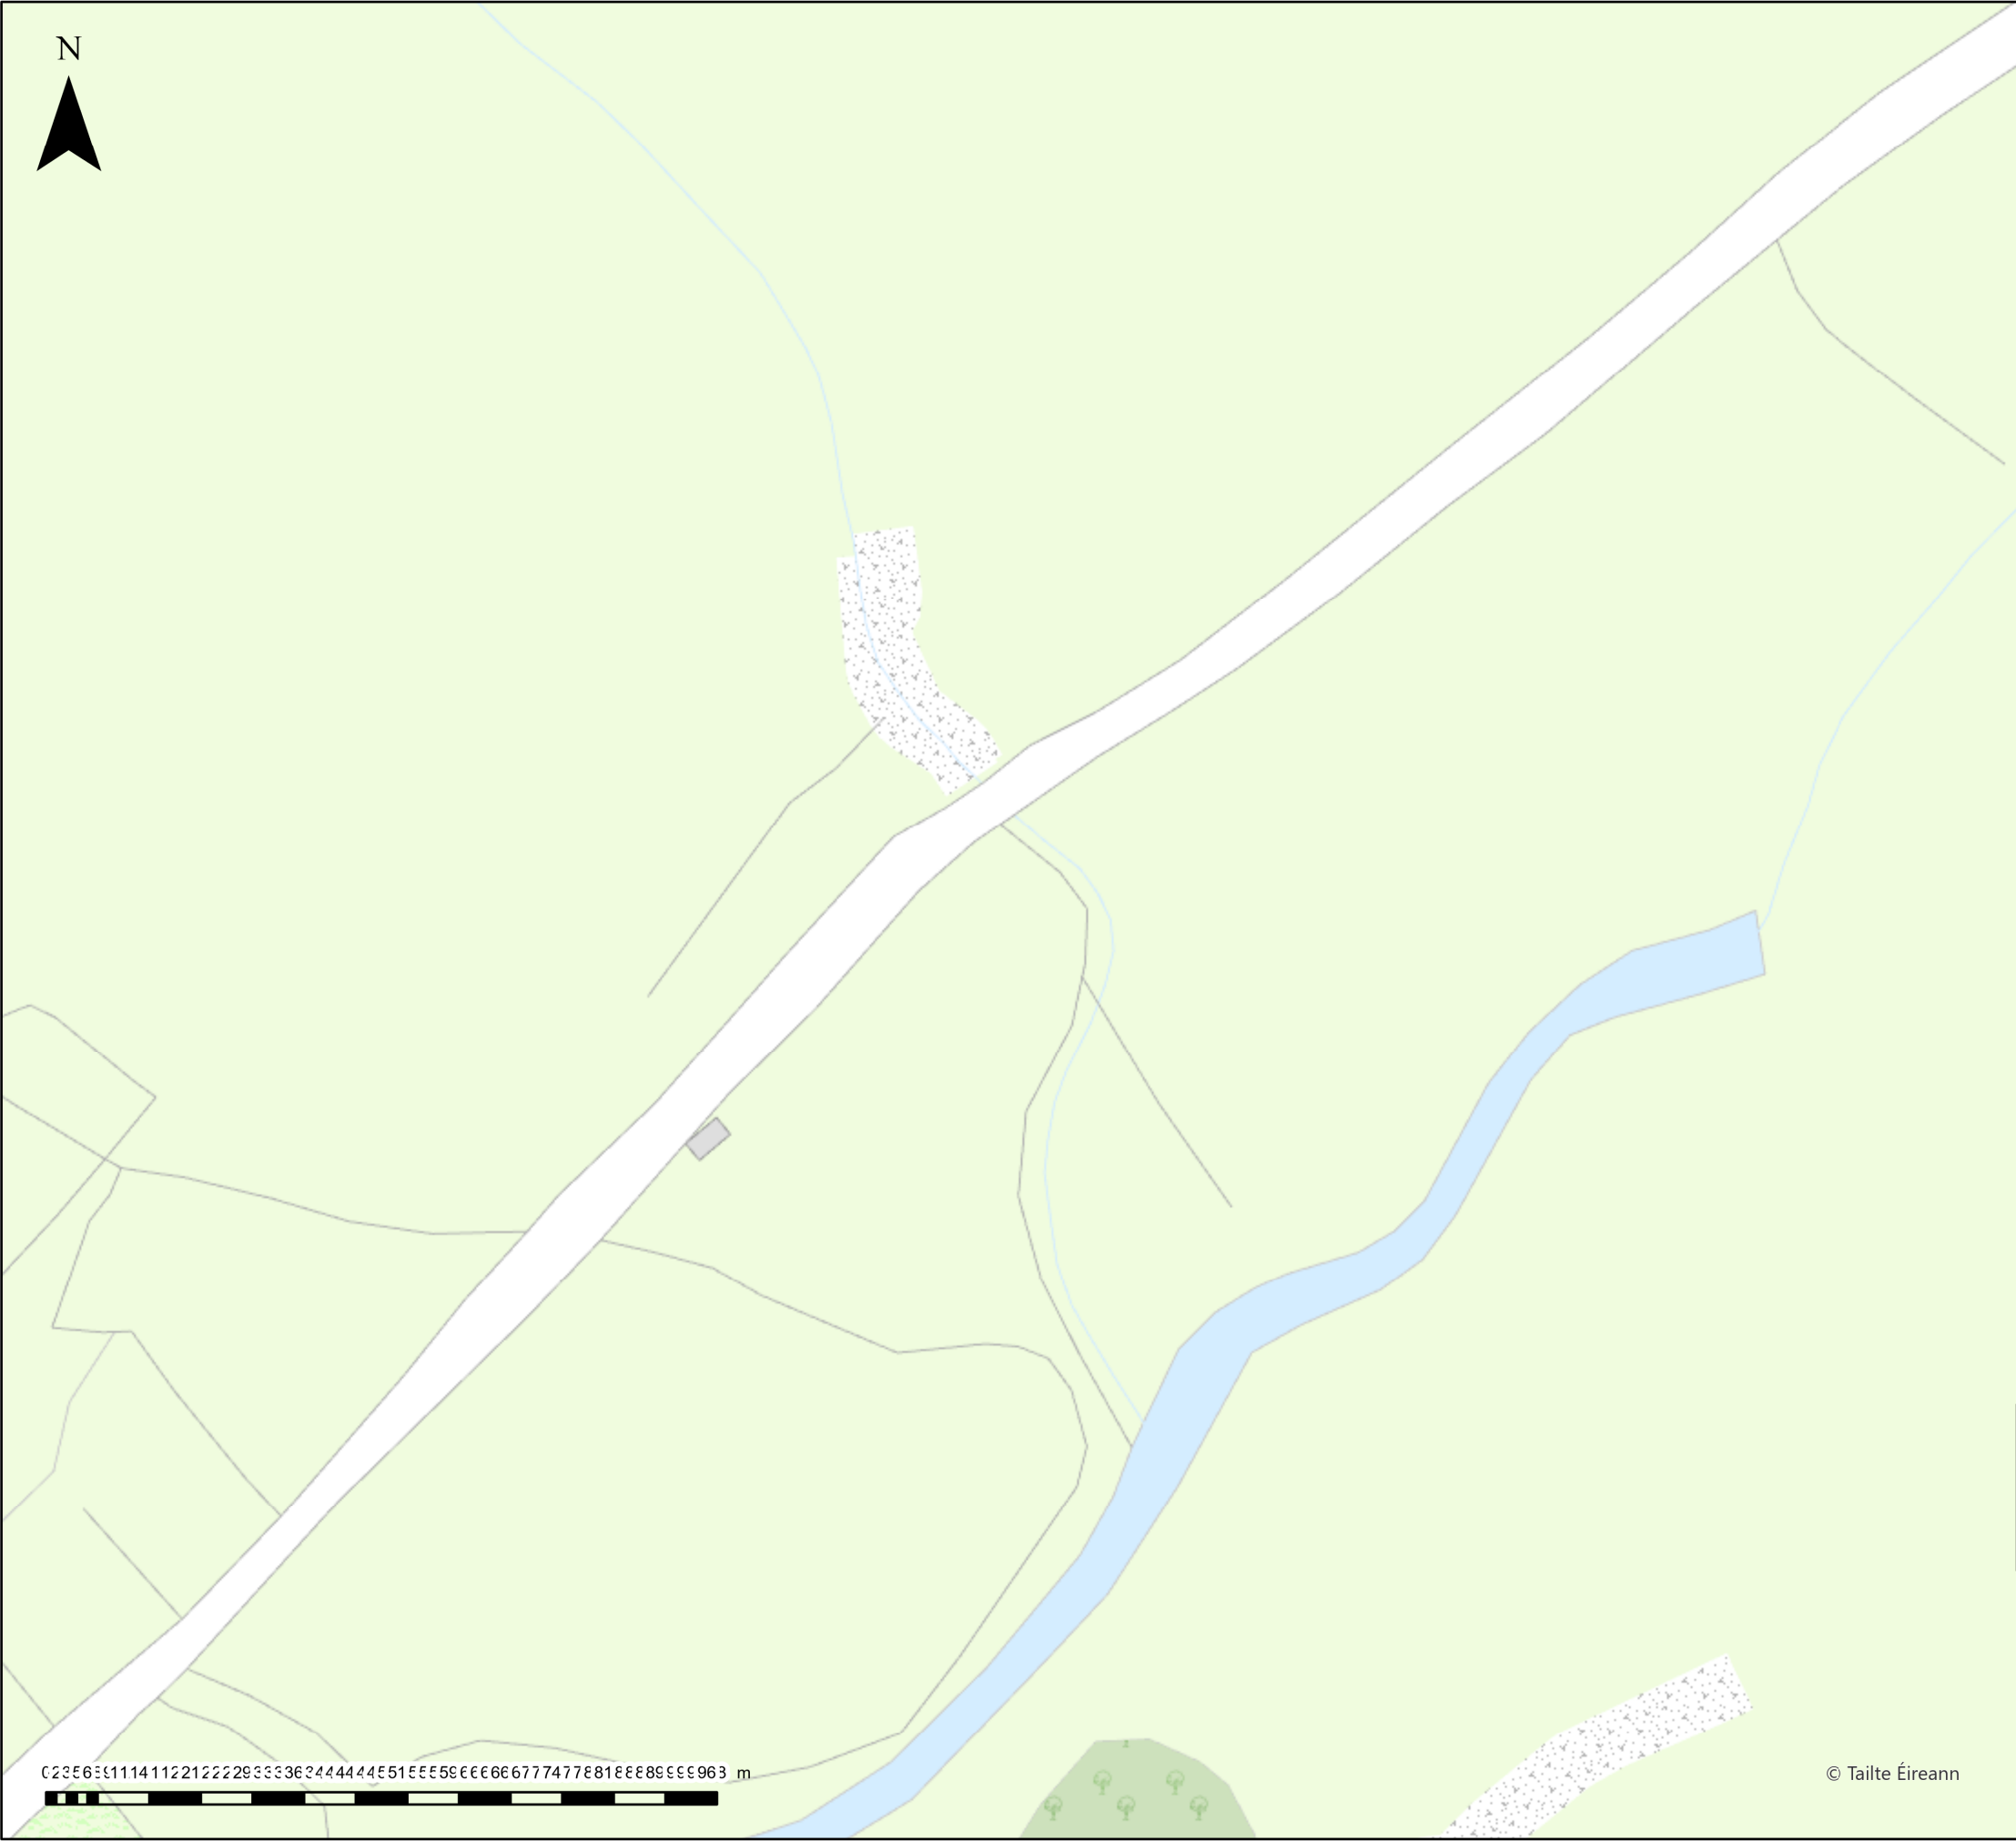

Important Safety Notice: Damage to gas pipelines can result in serious injury or death. Gas network information is provided as a general guide. The exact location and depth of medium or low pressure distribution gas pipes must be verified on site by carrying out necessary investigations, including, for example, hand digging trial holes along the route of the pipe. Service pipes are not generally shown but their presence should always be anticipated.

High pressure transmission pipelines are shown in red. If a transmission pipeline is identified within 10m of any intended excavations then work must not proceed before GNI has been consulted. The true location and depth of a transmission pipeline must be verified on site by a representative of GNI. Contact can be made through 1800 427 747.

All work in the vicinity of the gas network must be completed in accordance with the current edition of the Health and Safety Authority publication, 'Code of Practice For Avoiding Danger From Underground Services' which is available from the Health and Safety Authority (0818 289 389) or can be downloaded at www.hsa.ie.

Legal Notice: Gas Networks Ireland (GNI) and its affiliates, accept no responsibility for the accuracy of any information contained in this document including data concerning location and technical designation of the gas distribution and transmission network (the 'Information'). The Information should not be relied on for accurate distance or depth of cover measurements.

Any representations and warranties, express or implied, are excluded to the fullest extent permitted by law. No liability shall be accepted for any loss or damage including, without limitation, direct, indirect or consequential loss, arising out of or in connection with the use or re-use of the Information.

Reproduced from the Ordnance Survey by permission of the Government.
Licence No. 3-3-34

Aurora Telecom Duct

Aurora Telecom Sub Duct

Aurora Telecom Inserted Gas Pipe



Aurora Telecom Queries - 01-8926166 (Office Hours)
Aurora_Network_Queries@gasnetworks.ie
Aurora Telecom Emergency Only 1800 427399 / 01 2030120

Transmission Pipe (High Pressure)

Transmission Pipe (Construction Issue)

Distribution Pipe (Medium Pressure)

Distribution Pipe (Low Pressure)

Service Pipe (Medium Pressure)

Service Pipe (Low Pressure)

Strategic Pipe (Medium Pressure)

Strategic Pipe (Low Pressure)

Inserted

Abandoned Pipe

C=?

Cover (depth in metres)

Pressure Monitor

CP Test Point

Protection (Slabbing)

End Cap

Protection (Sleeve)

Hot Tap

Reducer

Installation

Service Terminator

Valve

Tee

Mains Verification**

Transition

**** Please contact GNI on 1800-427747 for specific information**



DIAL BEFORE YOU DIG
1800 42 77 47
In Emergency call 1800 20 50 50






GAS NETWORK INFORMATION

Description: test

Location: 590299,909779

Plot Date: 03/09/2024 10:13	Scale: 1000 @ A3
Plotted By: 7769	Ref ID: 7769_03092024101341

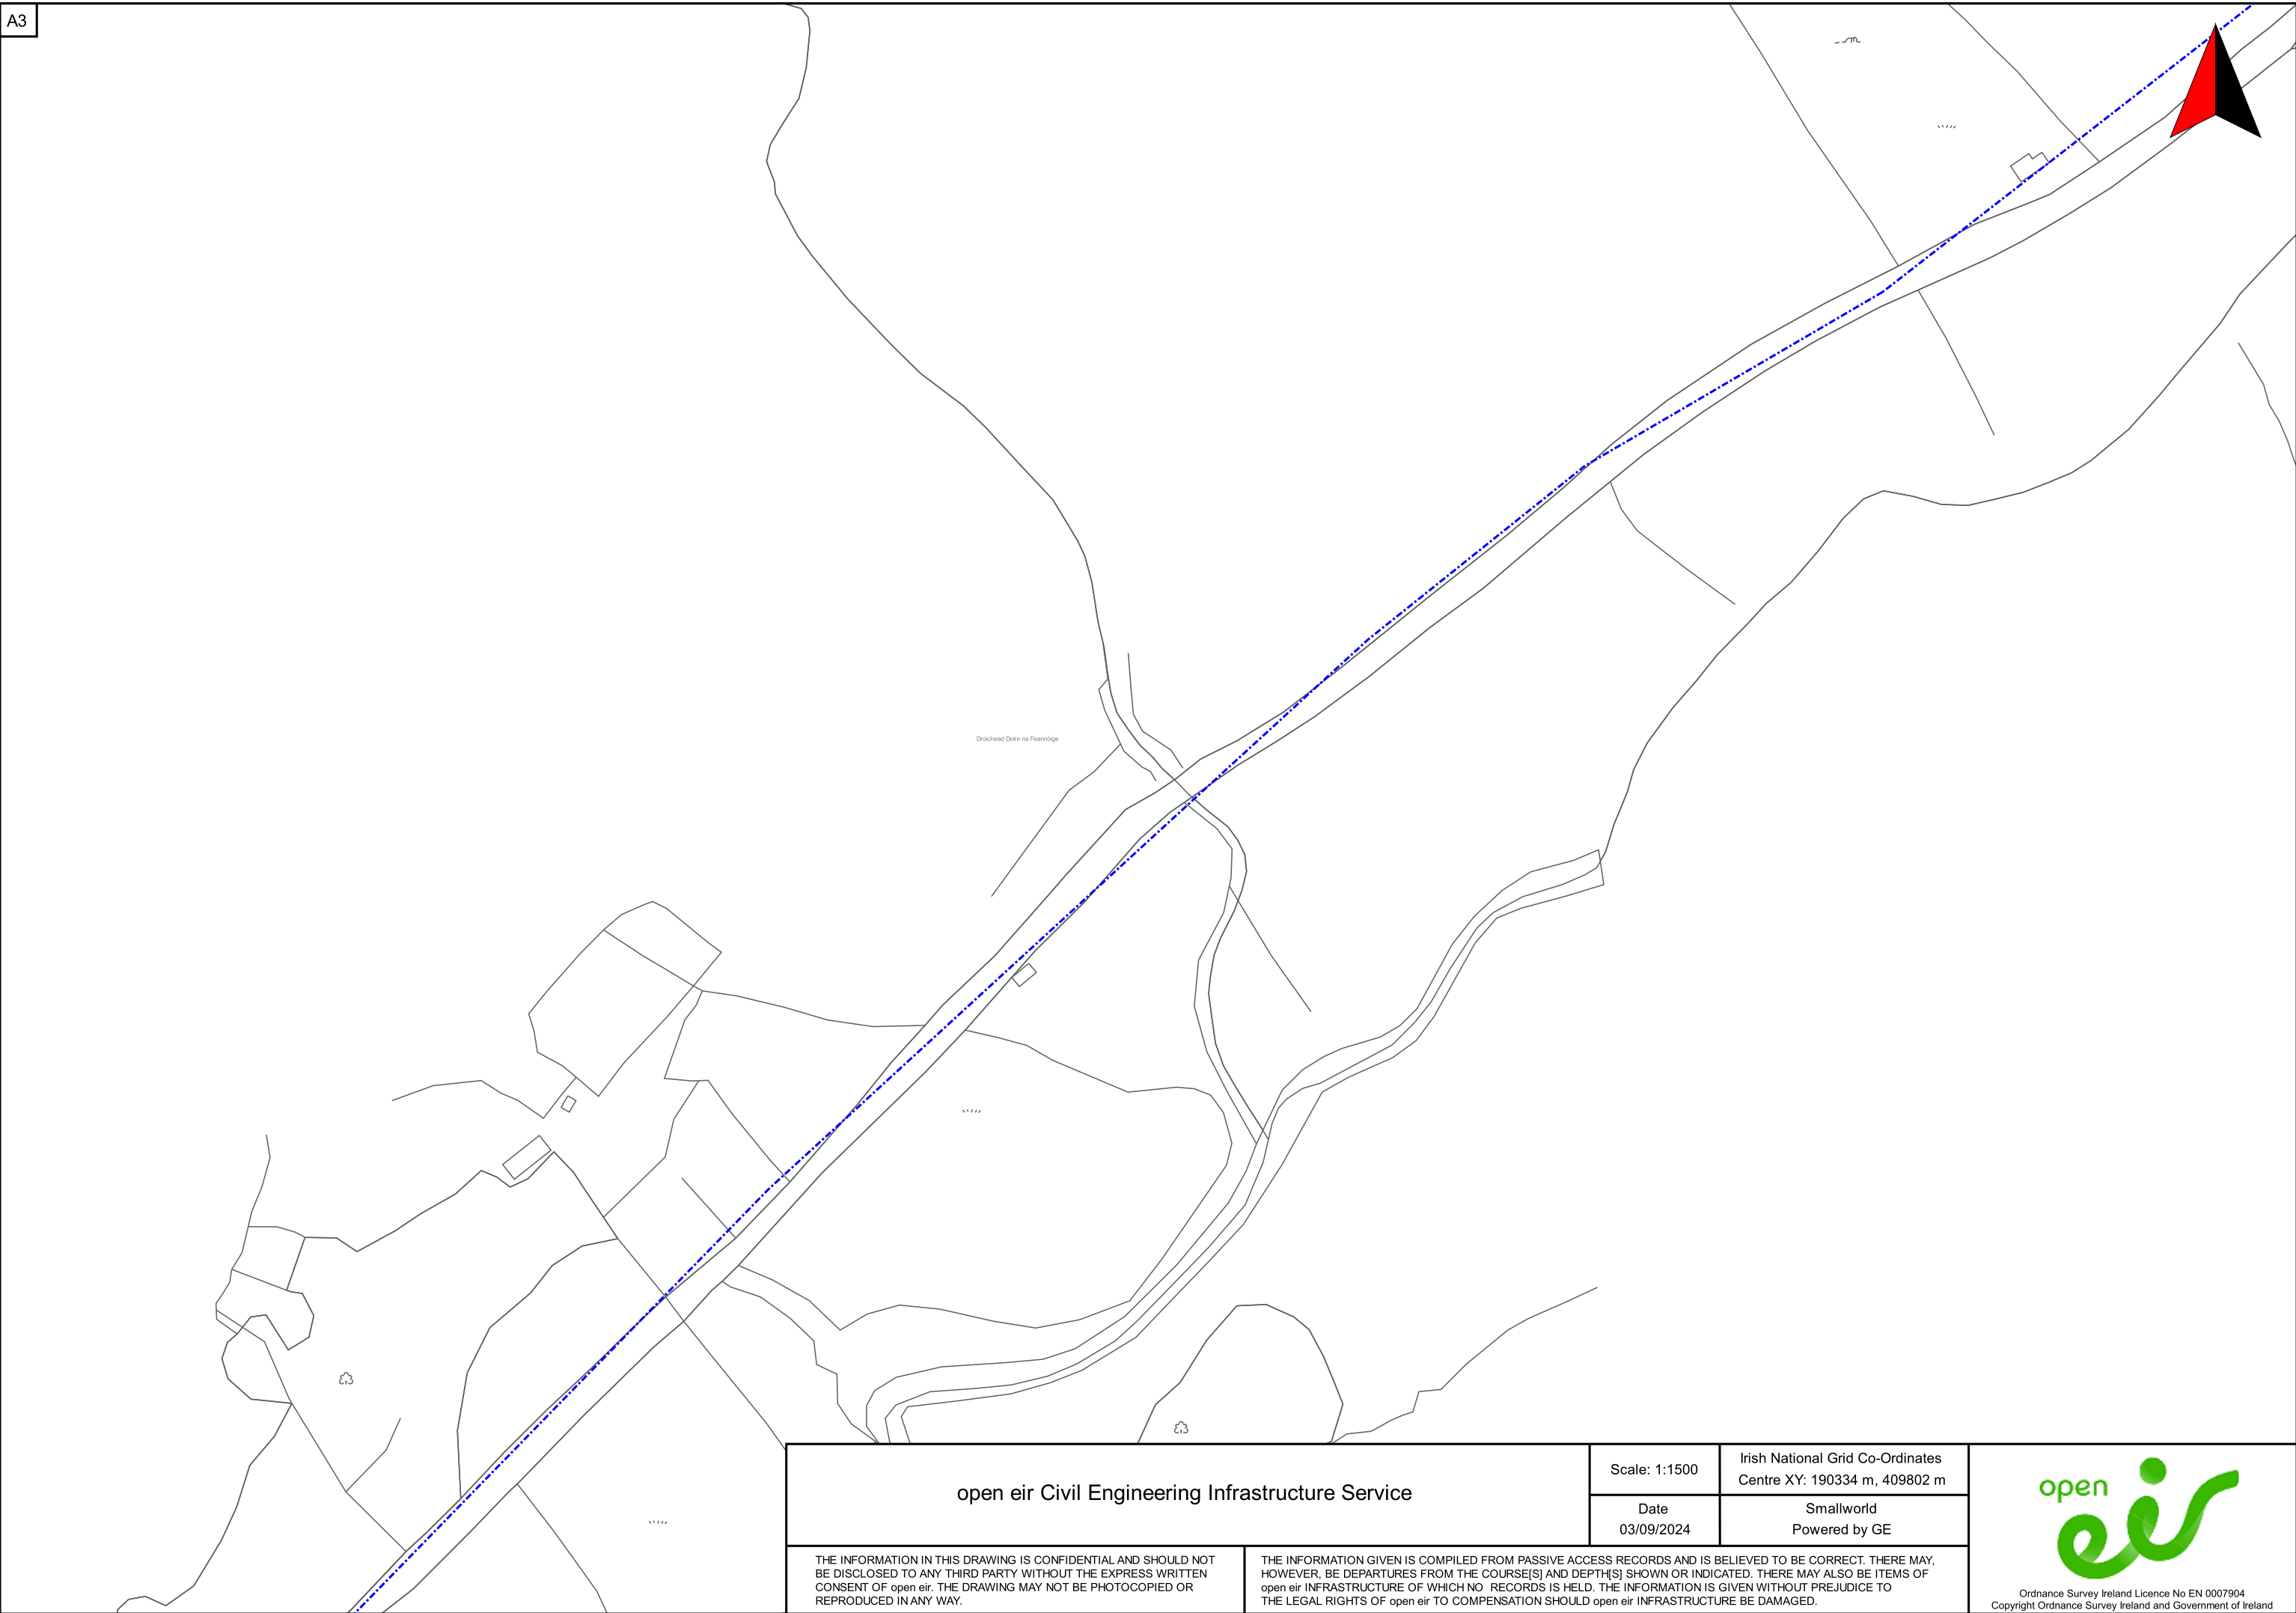

open eir Civil Engineering Infrastructure Service

Scale: 1:1500

Irish National Grid Co-Ordinates
Centre XY: 190334 m, 409802 m

Date
03/09/2024


Smallworld
Powered by GE

THE INFORMATION IN THIS DRAWING IS CONFIDENTIAL AND SHOULD NOT BE DISCLOSED TO ANY THIRD PARTY WITHOUT THE EXPRESS WRITTEN CONSENT OF open eir. THE DRAWING MAY NOT BE PHOTOCOPIED OR REPRODUCED IN ANY WAY.

THE INFORMATION GIVEN IS COMPILED FROM PASSIVE ACCESS RECORDS AND IS BELIEVED TO BE CORRECT. THERE MAY, HOWEVER, BE DEPARTURES FROM THE COURSE(S) AND DEPTH(S) SHOWN OR INDICATED. THERE MAY ALSO BE ITEMS OF open eir INFRASTRUCTURE OF WHICH NO RECORDS IS HELD. THE INFORMATION IS GIVEN WITHOUT PREJUDICE TO THE LEGAL RIGHTS OF open eir TO COMPENSATION SHOULD open eir INFRASTRUCTURE BE DAMAGED.




Ordnance Survey Ireland Licence No EN 0007904
Copyright Ordnance Survey Ireland and Government of Ireland

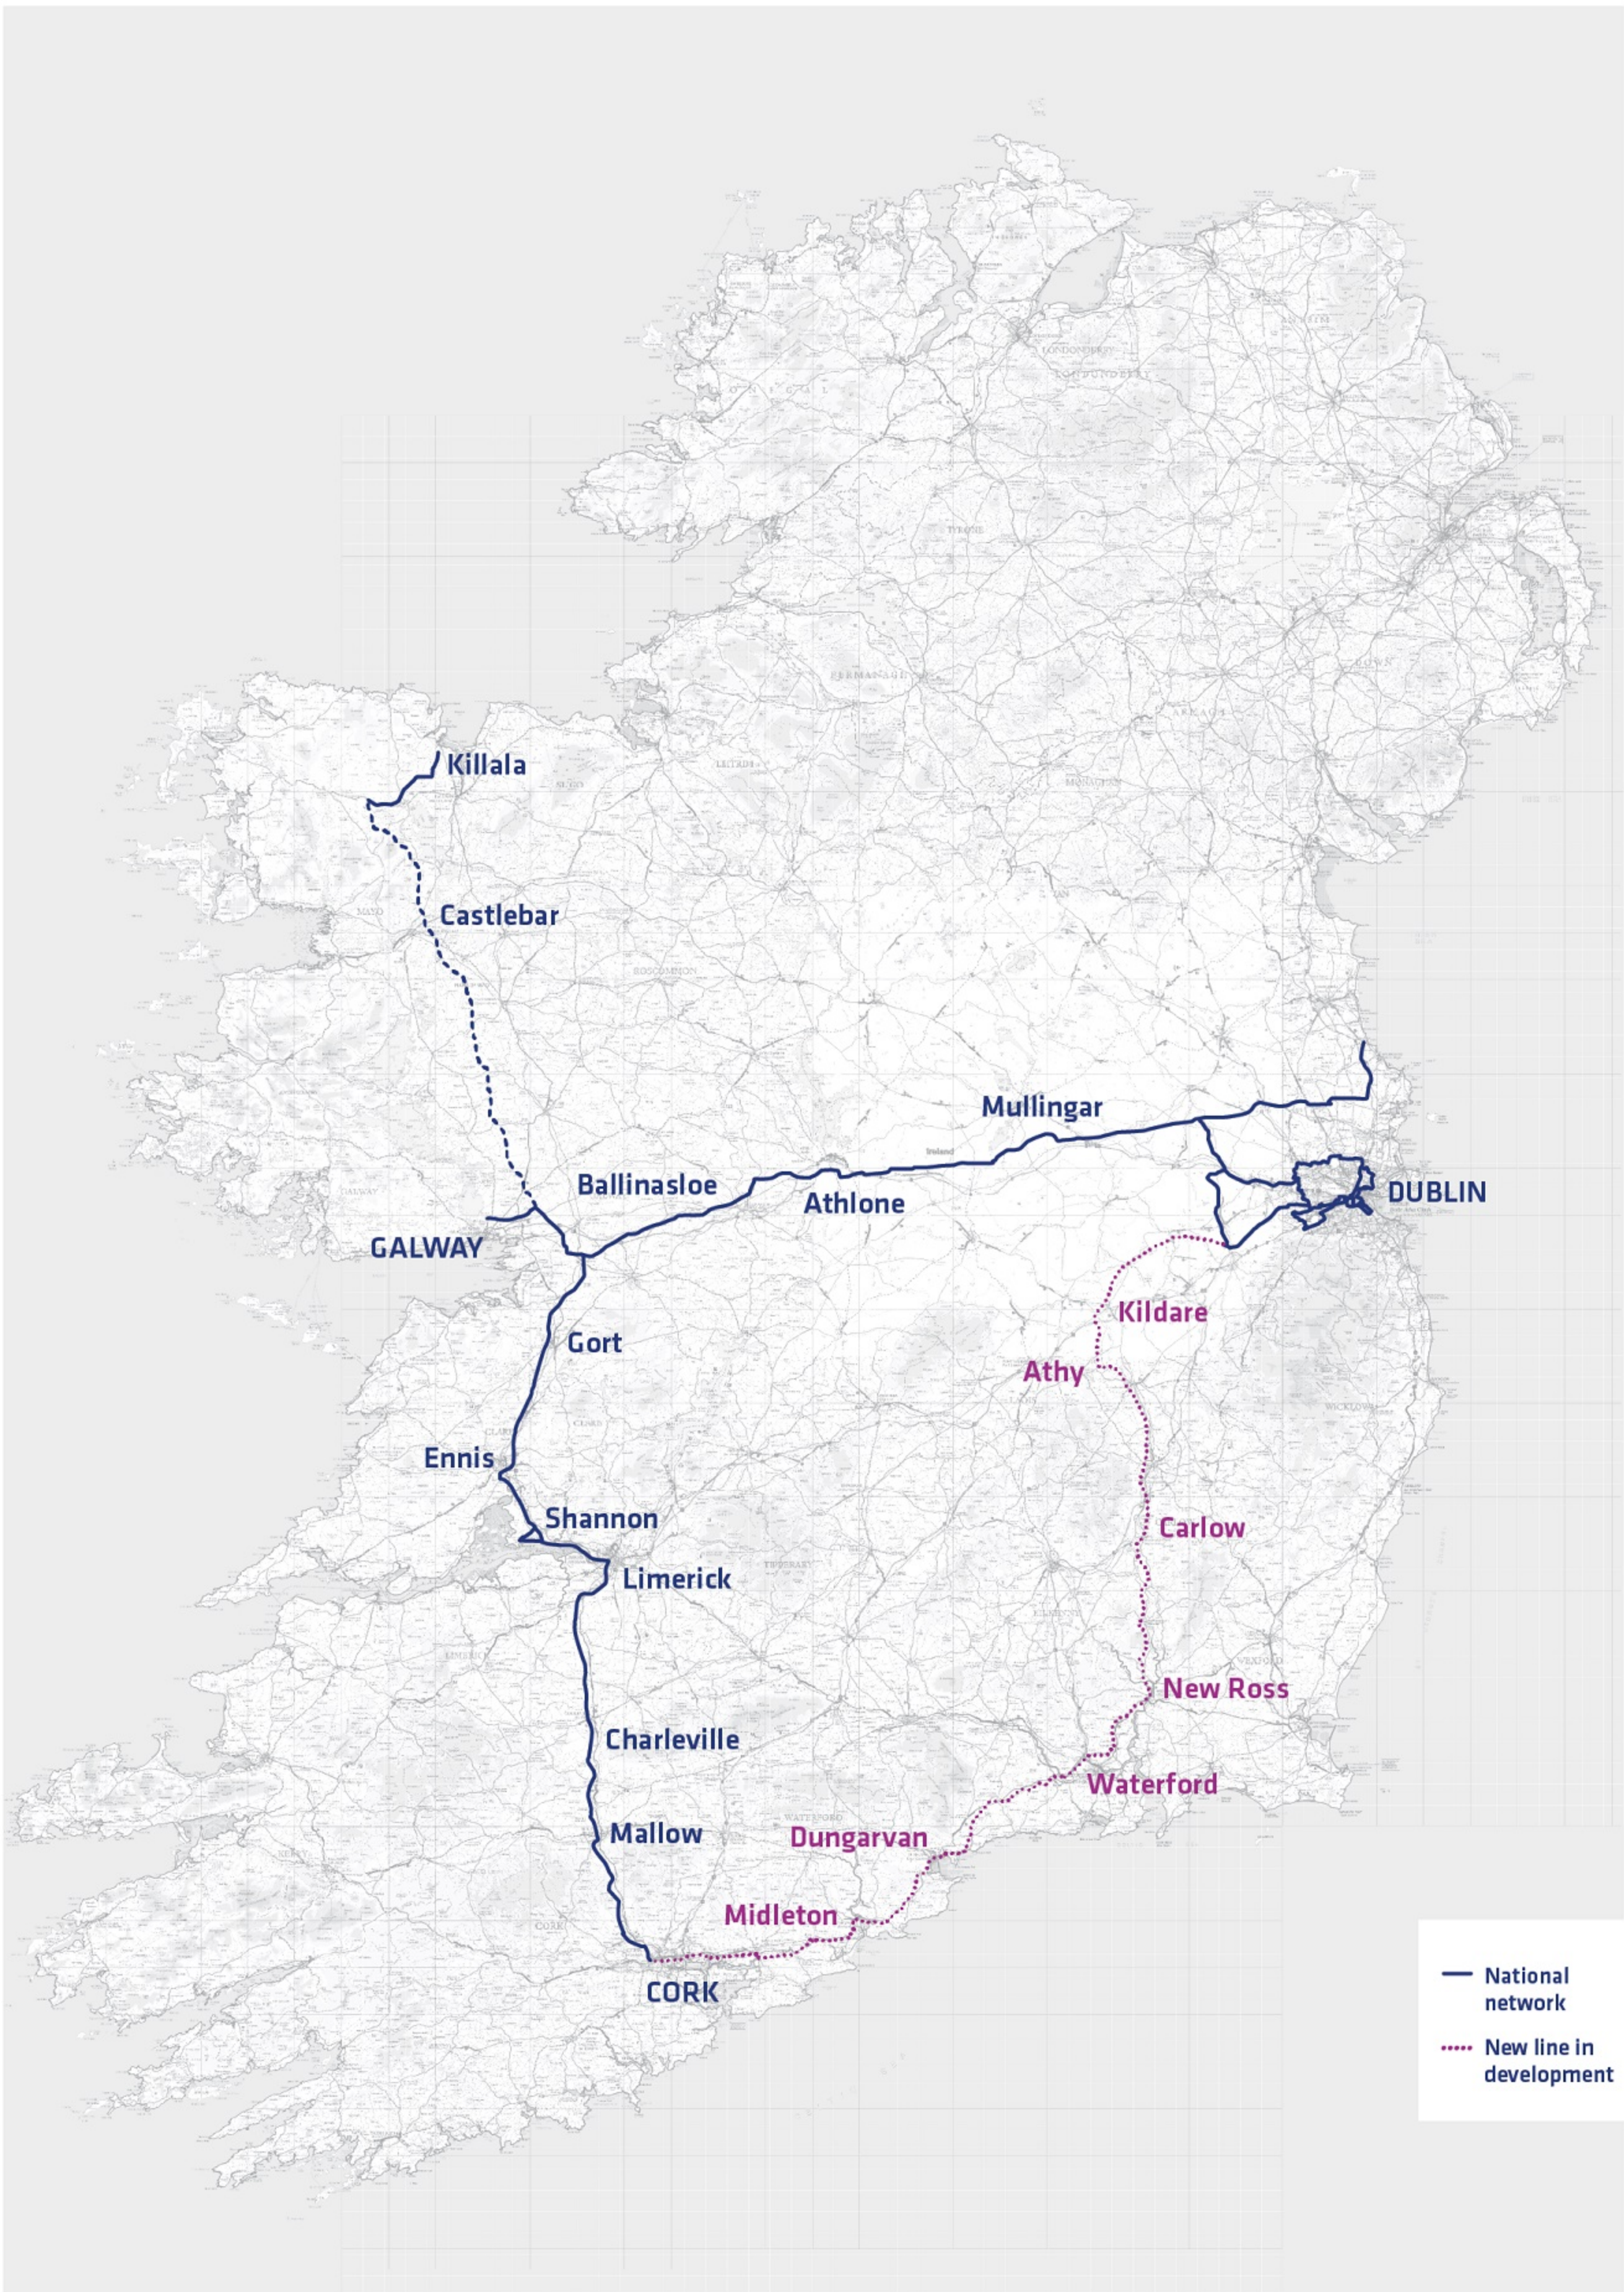

 National Fibre Network

 ESBT POP Sites


▼ All items

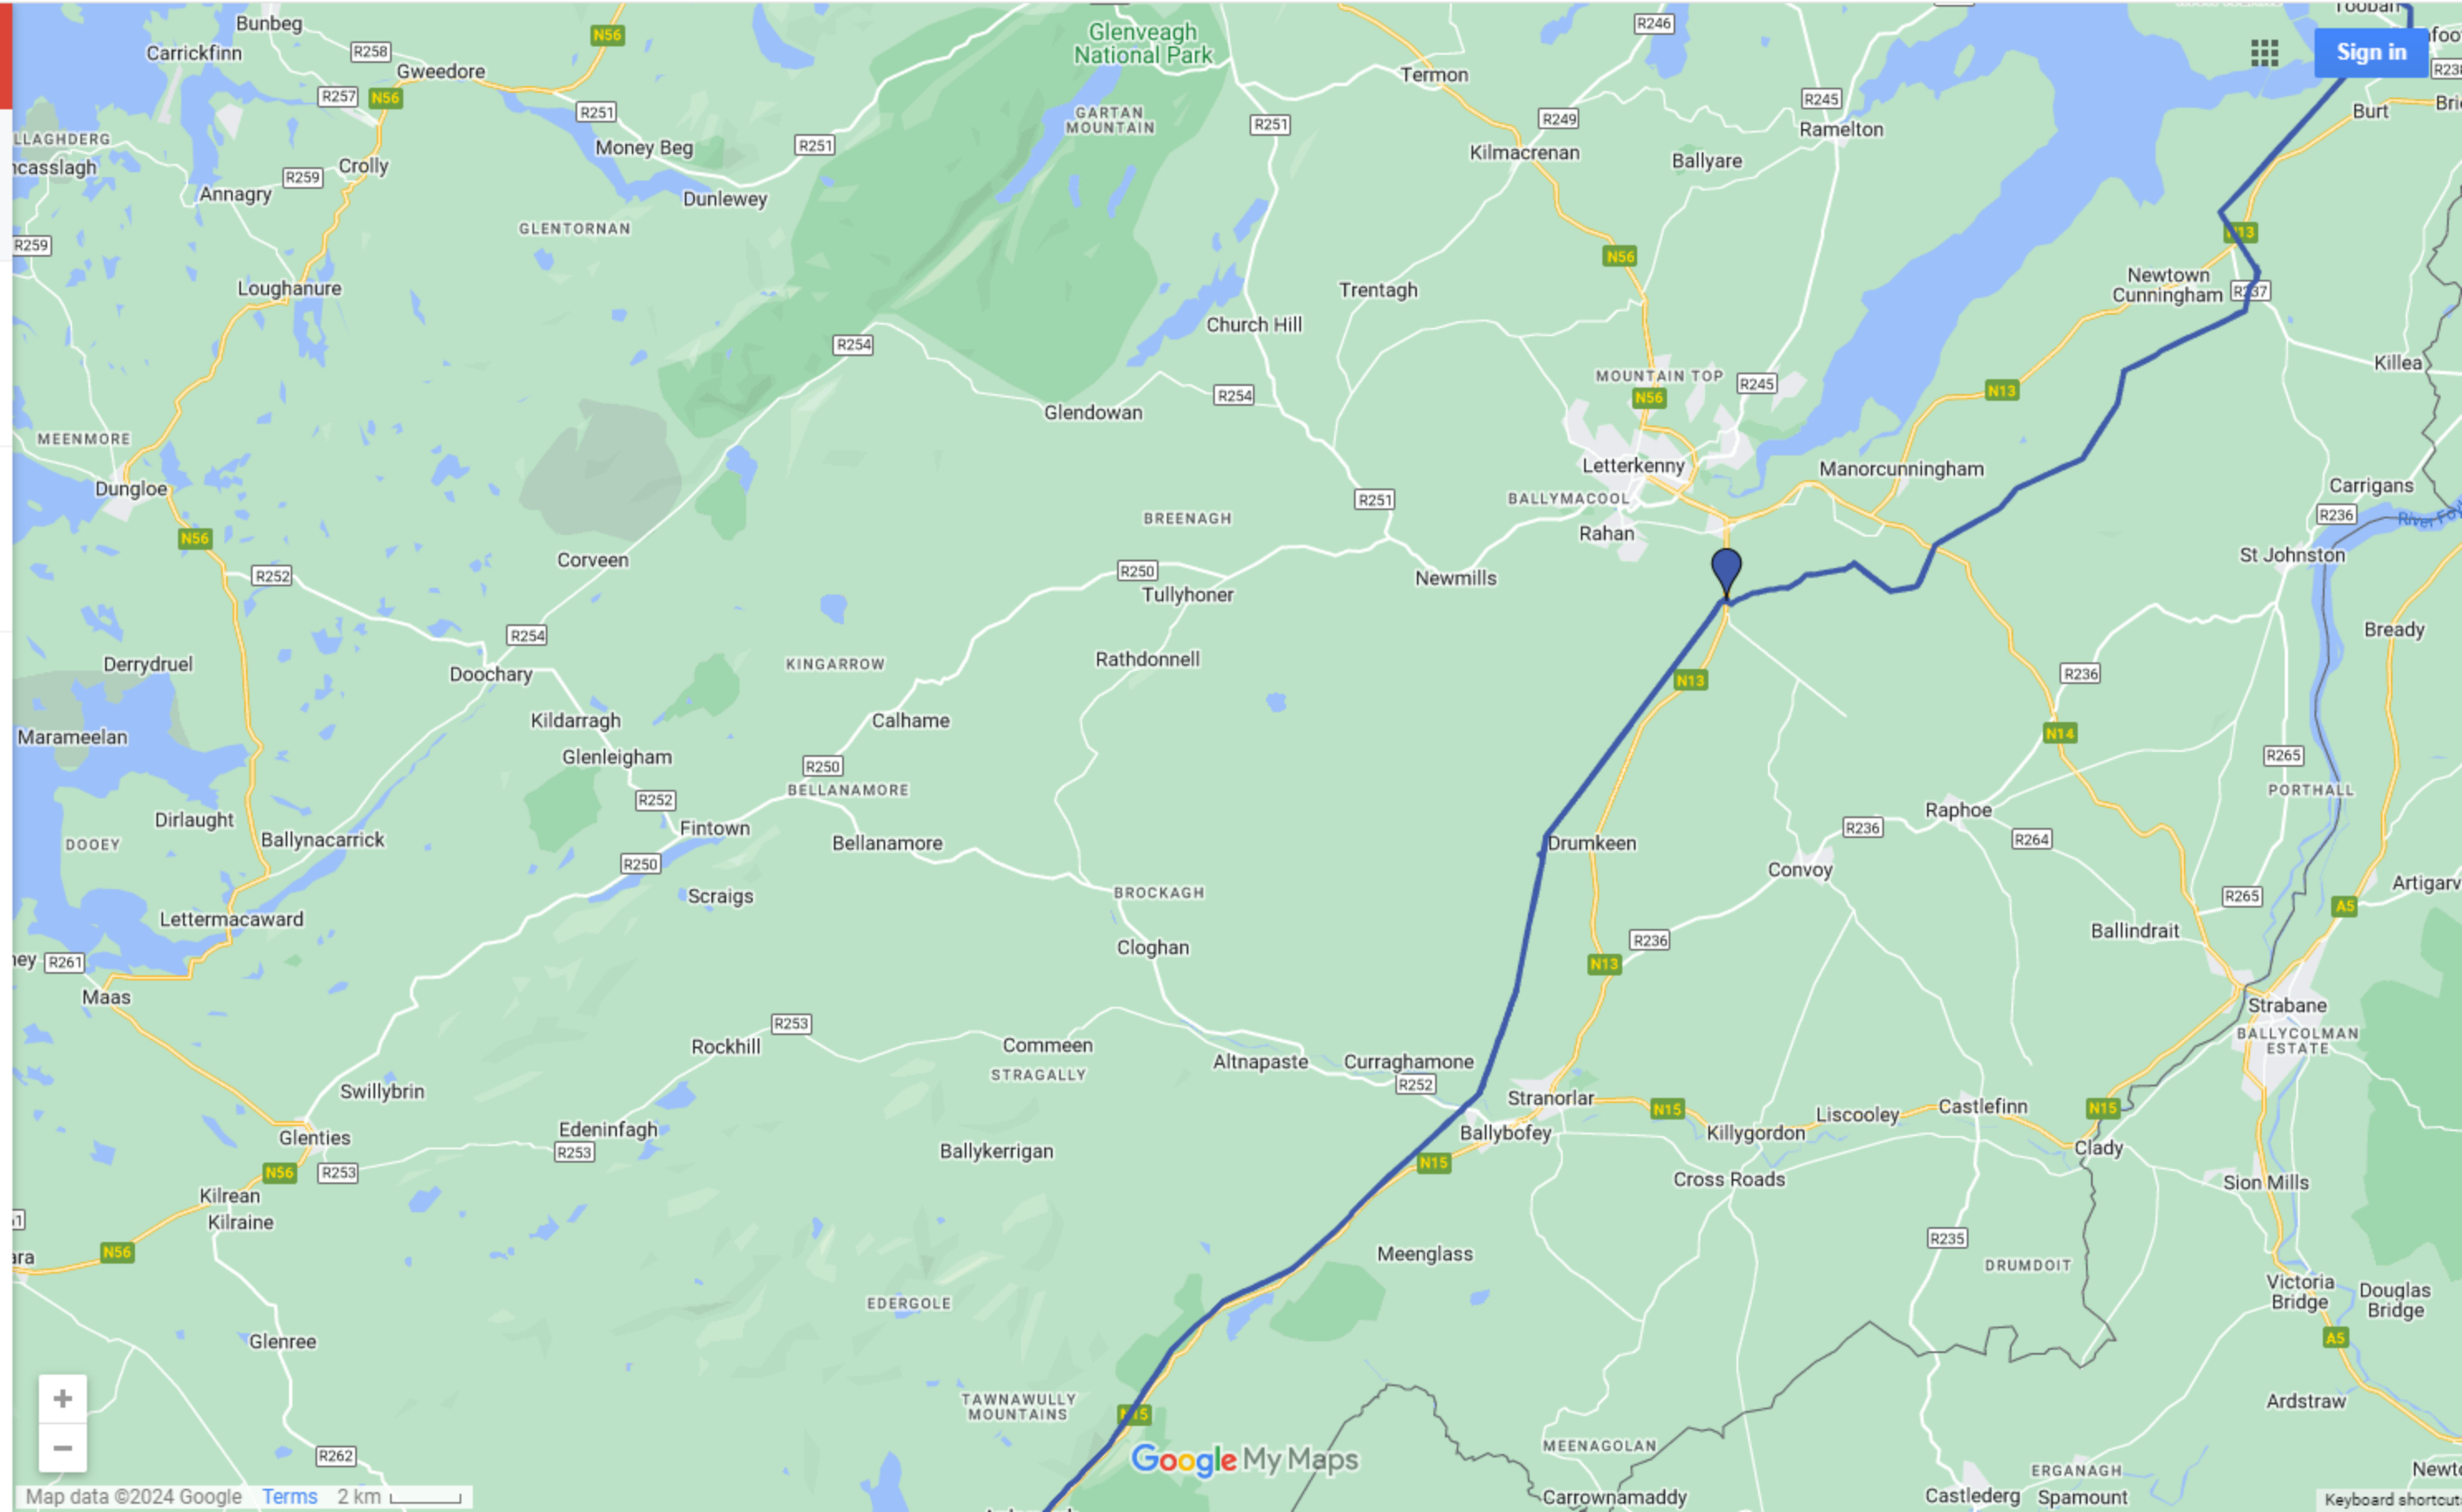

- National Fibre Network
- All items

ESBT POP Sites

All items

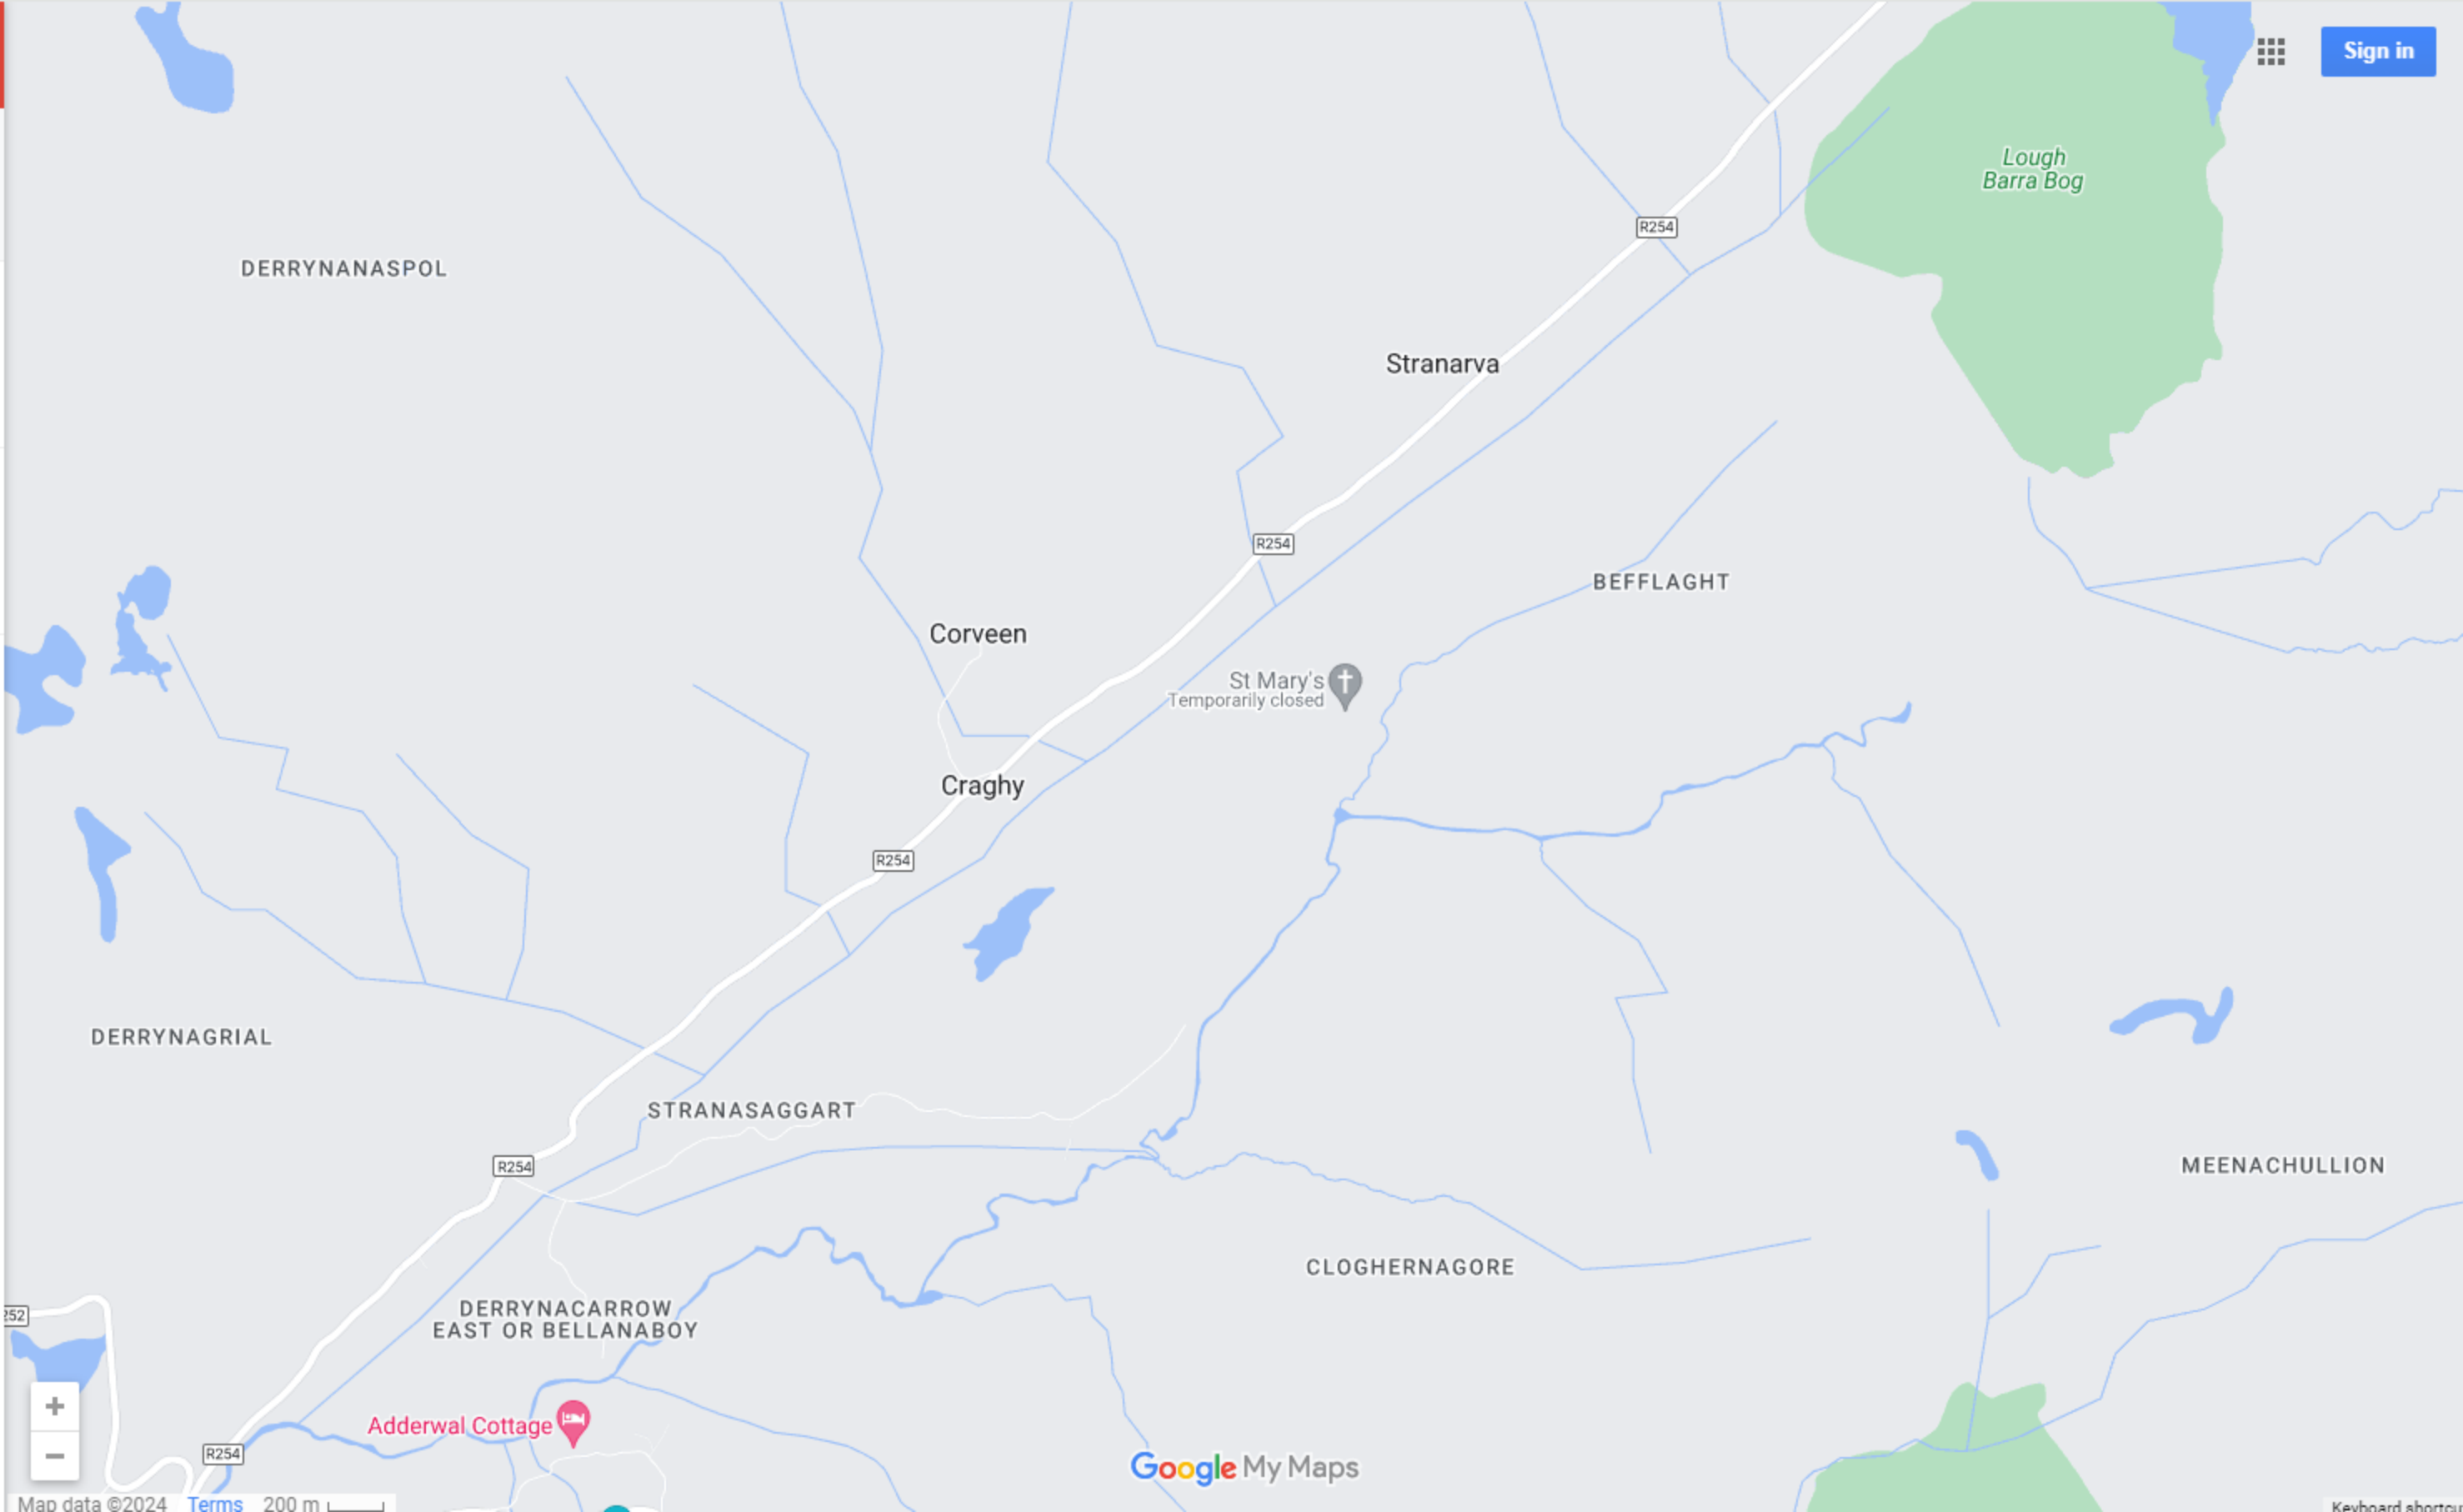

Ciara Conlon

From: Igor Blanaru <iblanaru@tibus.com>
Sent: 03 September 2024 13:38
To: Ciara Conlon
Cc: Ronan Carlin; Mark Rooney
Subject: Re: [#28027] 24200 - Dernafanogy Bridge Tibus Information Request

This Message originated outside your organisation.

Hi Ciara,

We don't have any premises in Doochary area

Kind Regards
Igor

--


IGOR BLANARU
Lead Customer Support Engineer
Tibus

T: +44 (0)28 9033 1122
E: iblanaru@tibus.com
W: www.tibus.com

Tibus is a wholly-owned division of Wireless.



This is a response to ticket **[#28027] (24200 - Dernafanogy Bridge Tibus Information Request)** by **Igor Blanaru** from Tibus Support. To respond please reply to this email.

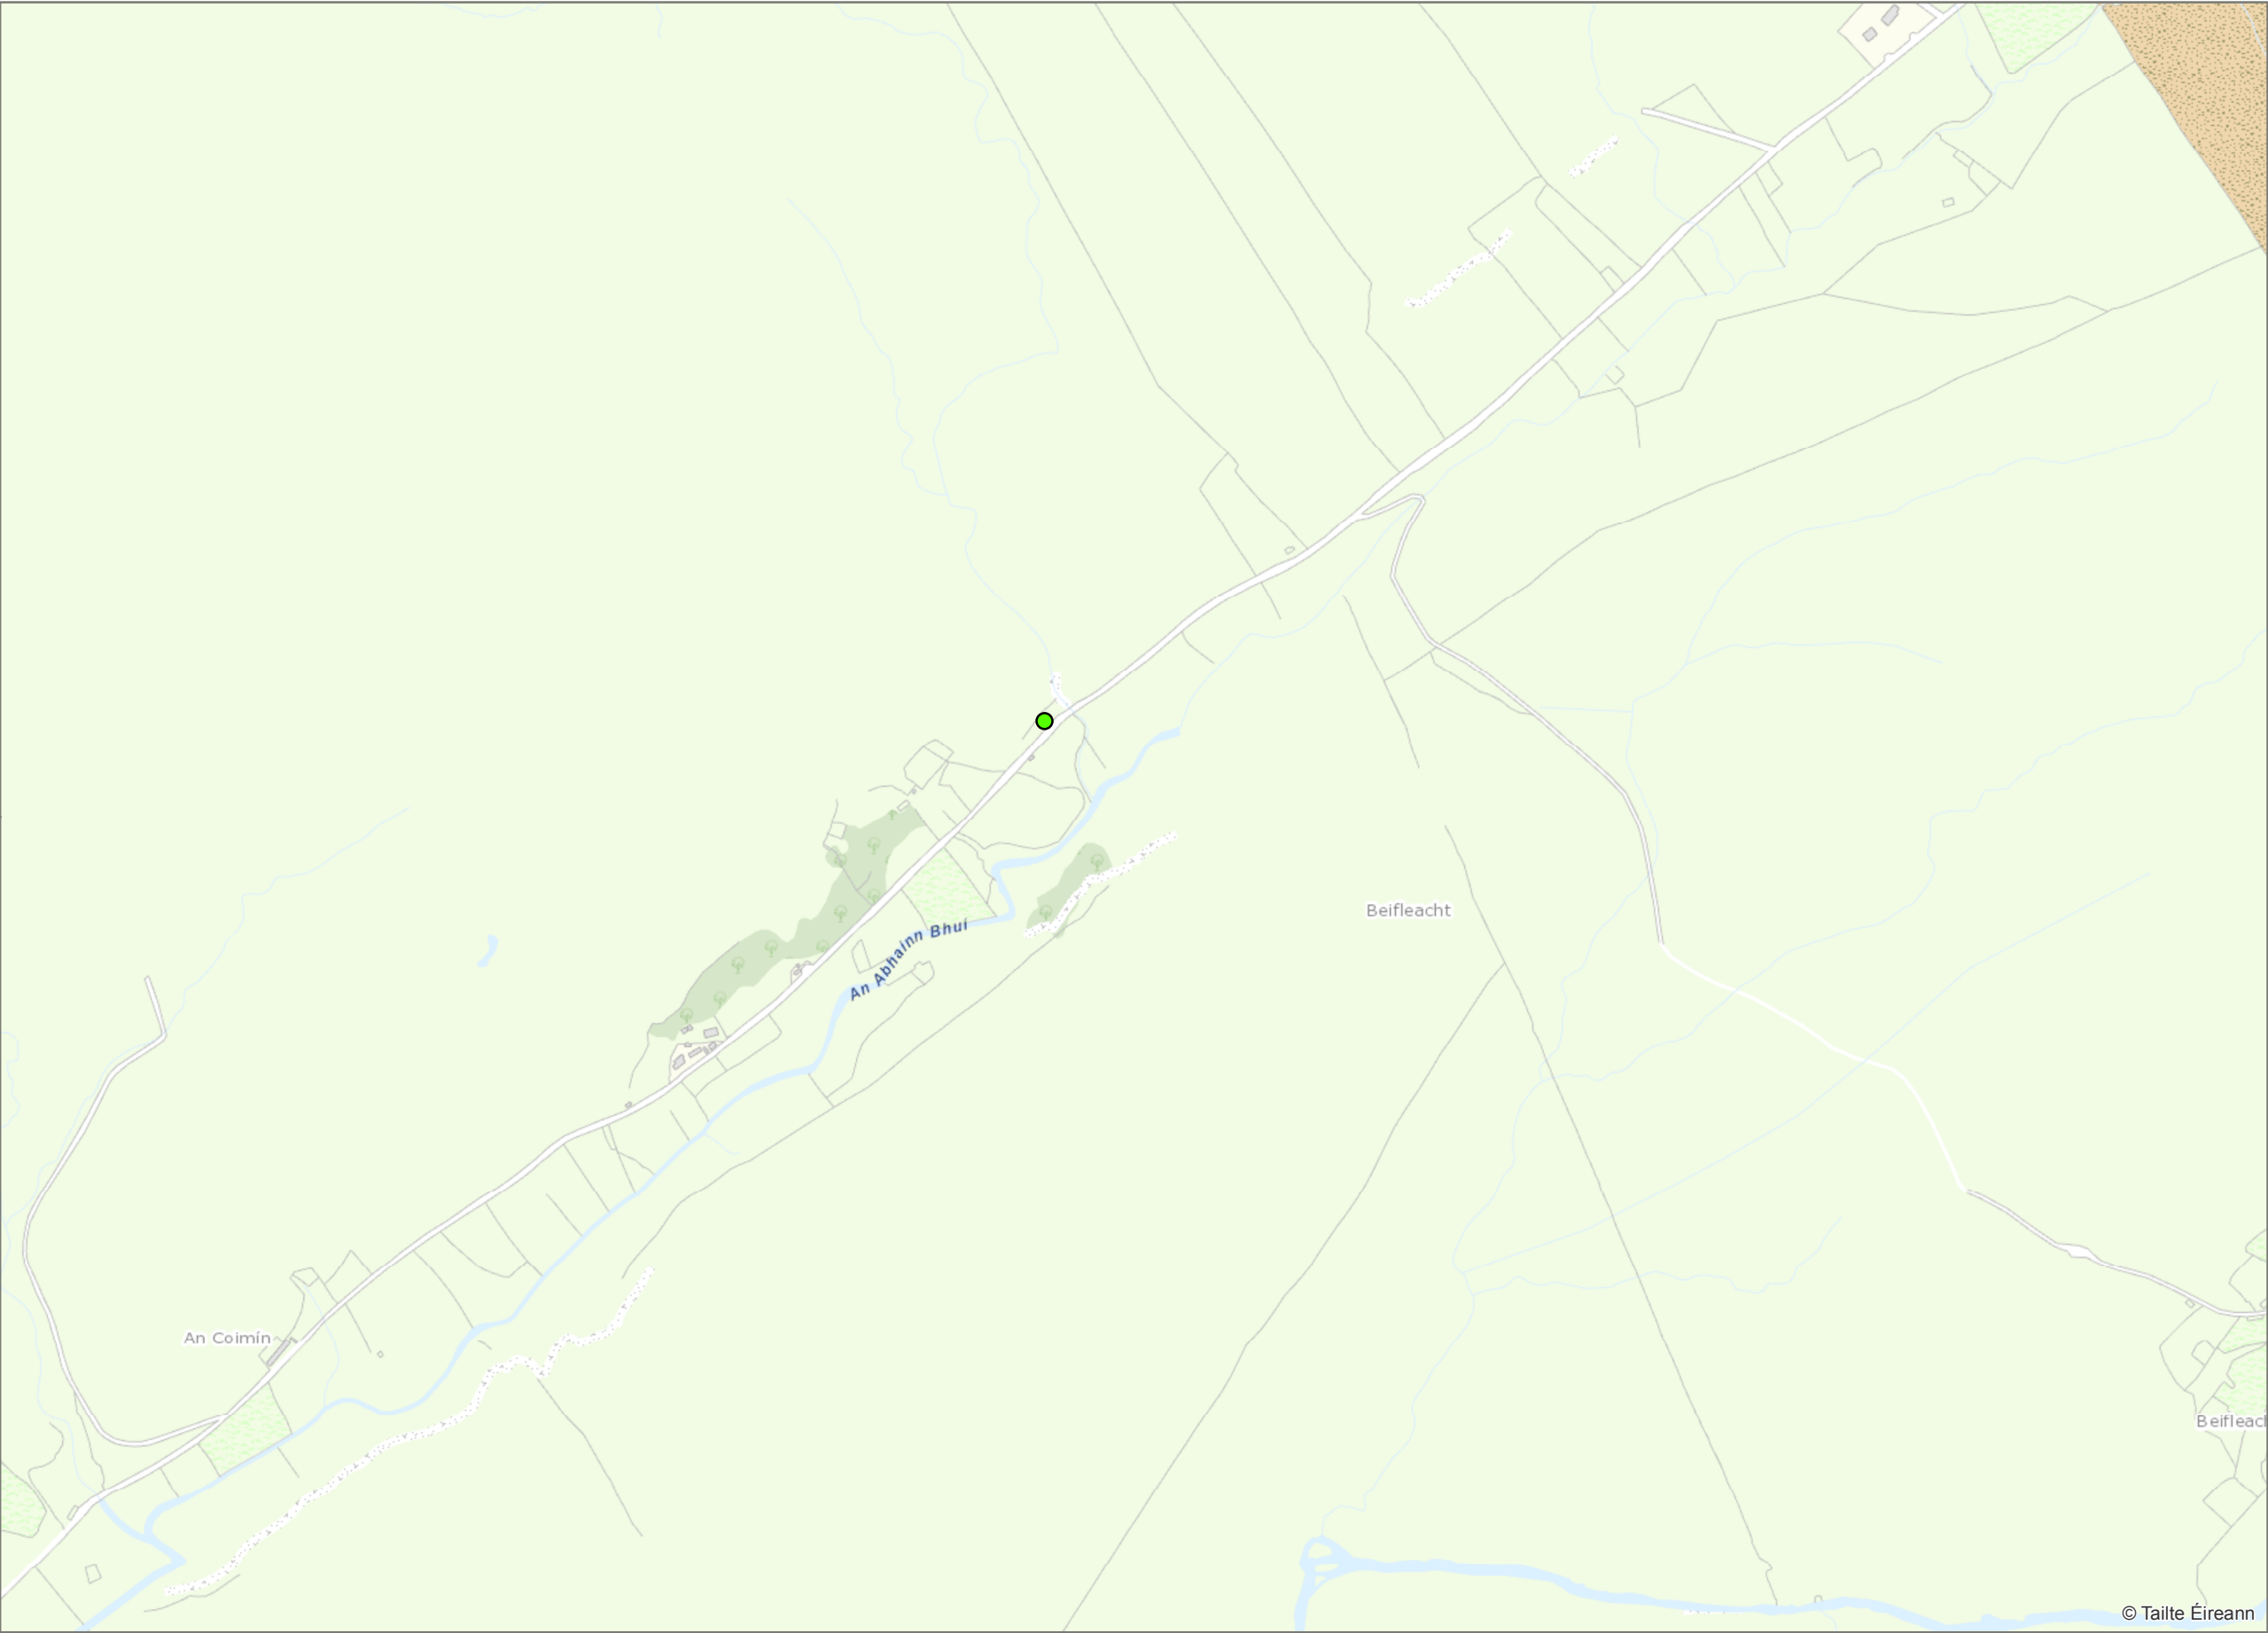

Legend

055110220m	
Coordinate System: TM65 Irish Grid Projection: Transverse Mercator	
Scale @ A3:	1:6,911
Drawing No.:	IW-AGG-2018-000
Drawn By:	Mo Ismail
Checked By:	<Add Name>
Approved By:	<Add Name>
Drawn Date	05/09/2024
Checked Date:	<dd/mm/yyyy>
Approved Date:	<dd/mm/yyyy>



1. No part of this drawing may be reproduced or transmitted in any form or stored in any retrieval system of any nature without the written permission of Irish Water as copyright holder except as agreed for use on the project for which the document was originally issued.

2. Whilst every care has been taken in its compilation, Irish Water gives this information as to the position of its underground network as a general guide only on the strict understanding that it is based on the best available information provided by each Local Authority in Ireland to Irish Water. Irish Water can assume no responsibility for and give no guarantees, undertakings or warranties concerning the accuracy, completeness or up to date nature of the information provided and does not accept any liability whatsoever arising from any errors or omissions. This information should not be relied upon in the event of excavations or any other works being carried out in the vicinity of the Irish Water underground network. The onus is on the parties carrying out excavations or any other works to ensure the exact location of the Irish Water underground network is identified prior to excavations or any other works being carried out. Service connection pipes are not generally shown but their presence should be anticipated.

© Copyright Irish Water

Reproduced from the Ordnance Survey Of Ireland by Permission of the Government. License No. 3-3-34

Water and Sewer network
Dernaflanogy Bridge, Co.Donegal
